

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF FEBRUARY 2024

WORK COMPLETED AND ONGOING:

Site

- City sidewalk installation – 95% complete
- Sod installation ongoing

Building

- Freezer/cooler installation complete
- Framing complete – Area 4
- Drywall tape and bed ongoing – Area 4
- Tile installation ongoing – Kitchen (Area 4)
- One-siding drywall ongoing – Areas 3 and 4
- MEP rough-in ongoing – Areas 1 and 2
- Building is 100% dried in



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF FEBRUARY 2024



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF FEBRUARY 2024



Main Entry



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF FEBRUARY 2024

Main Entry



Reception Area



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF FEBRUARY 2024

Main Entry Corridor



Academic Corridor

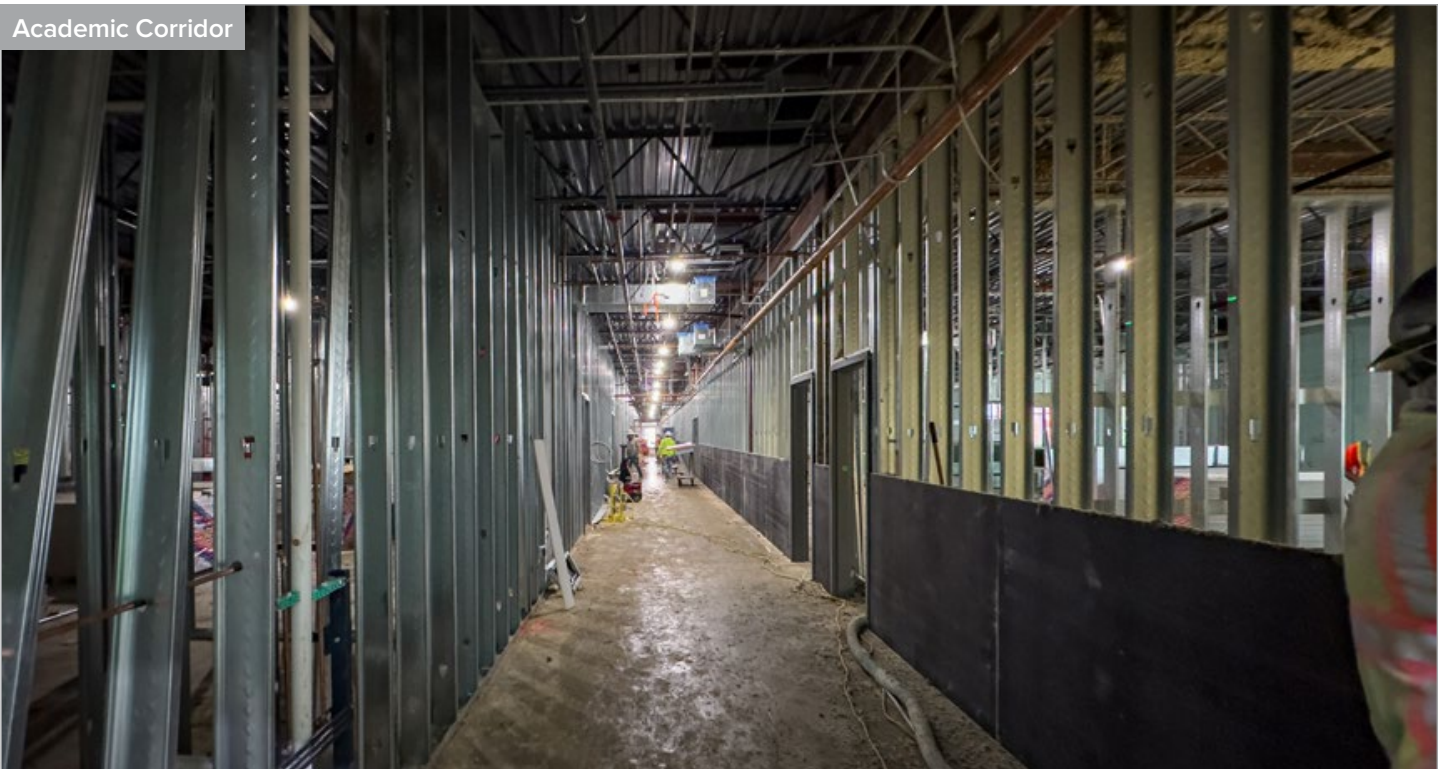

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF FEBRUARY 2024

Classroom



Teaching Wall Mock-up



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF FEBRUARY 2024

Library



Secondary Corridor (Gymnasium/Cafetorium)



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF FEBRUARY 2024

Gymnasium (Shelter)



Cafetorium



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF FEBRUARY 2024

Kitchen



Rear Entry



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2024

WORK COMPLETED AND ONGOING:


Site

- Football field subgrade preparation complete
- Track and football field flatwork installation ongoing
- Track subgrade preparation ongoing; surface to be installed
- Tennis court fencing complete
- Tennis court flatwork complete; bleachers will be delivered and installed this month
- Sidewalk installation along Hardy Drive ongoing
- Pump house and concession stand veneer and roof complete; roof consultant punch list issued and corrections ongoing
- Final grading and topsoil installation ongoing
- Irrigation installation ongoing

Building

- Exterior sheathing complete
- Weather barrier installation ongoing – Area 8
- Storefront window installation ongoing – Area 8; installation complete – Areas 1-7, and 9-11
- MEP rough-in ongoing – Area 1-11

- Final overhead rough-in inspections called for – Areas 1-3, and 9-11; technology consultant punch list issued and corrections ongoing
- Permanent power transformer has been set; connection to temporary switchgear and meter set to take place this week
- Finishing gas line and meter installation this week
- Interior wall framing ongoing – Areas 4 and 8
- Two-siding drywall complete – Areas 9, 10 and 11
- Drywall tape, bed, and paint ongoing – Areas 7-11
- Tile installation ongoing in multi-user restrooms and academic corridors
- Classroom carpet installation ongoing
- Classroom millwork installation ongoing
- Science lab casework installation ongoing
- Tornado Shelter MEP rough-in ongoing
- Exterior veneer ongoing – Areas 4, 8, 9, 10 and 11
- Roofing ongoing – Area 8; installation complete – Areas 1-7, and 9-11

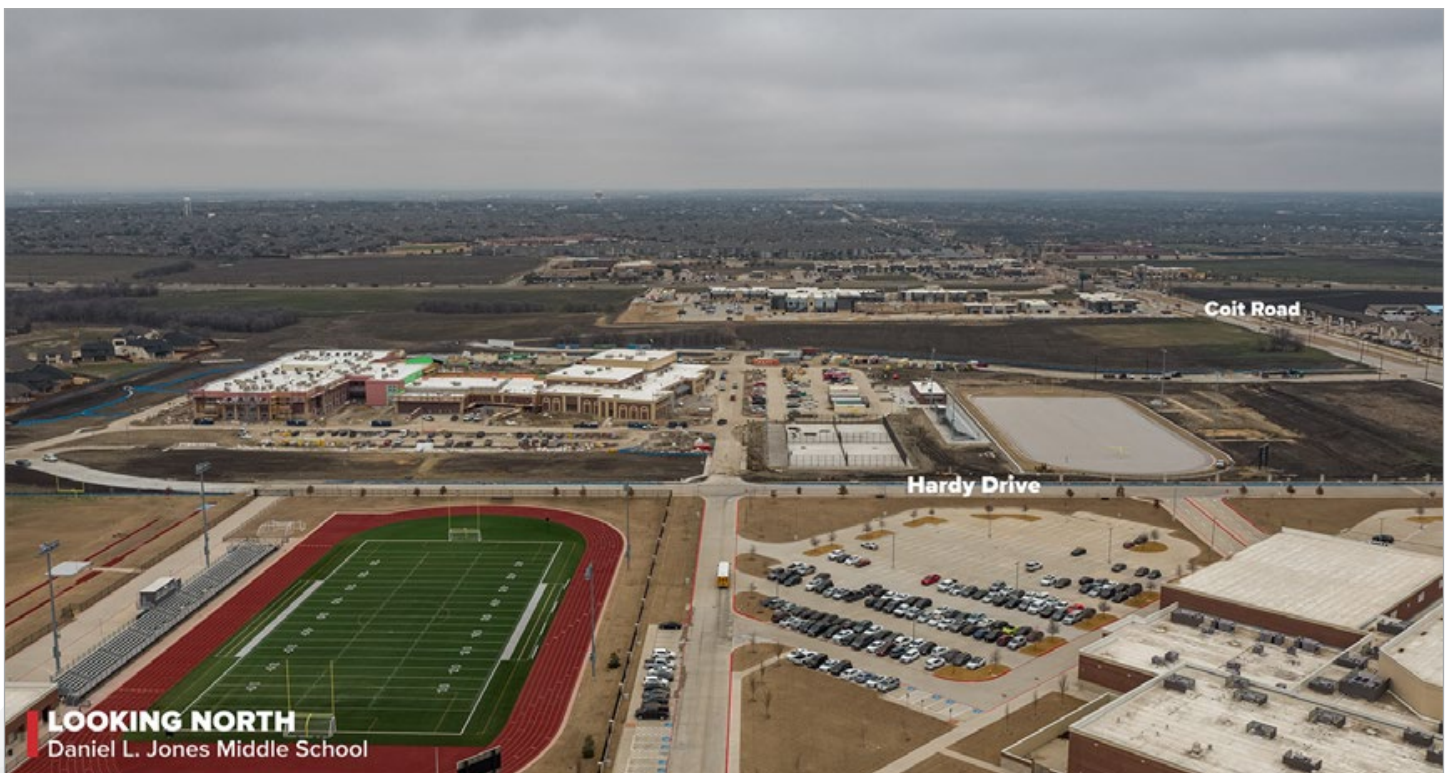

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2024



LOOKING EAST
Daniel L. Jones Middle School



LOOKING SOUTH
Daniel L. Jones Middle School

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2024



Entry Approach



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2024

Main Entry



Main Entry



BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2024

Main Entry (Interior)

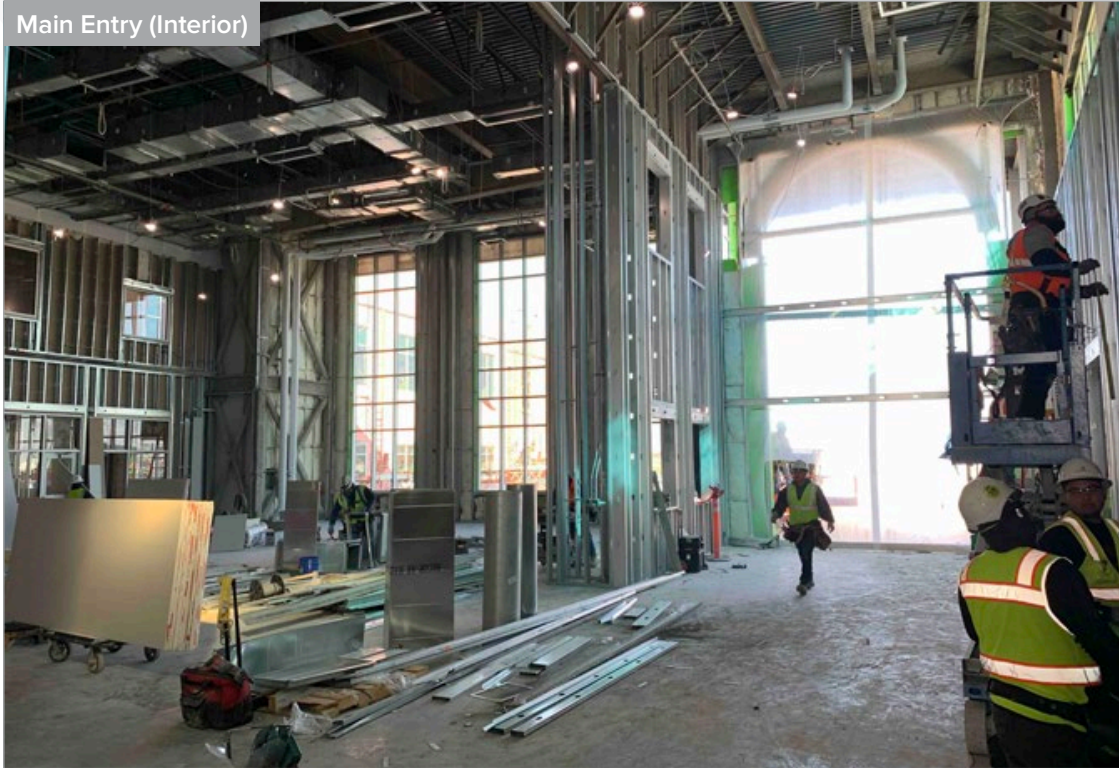

Library

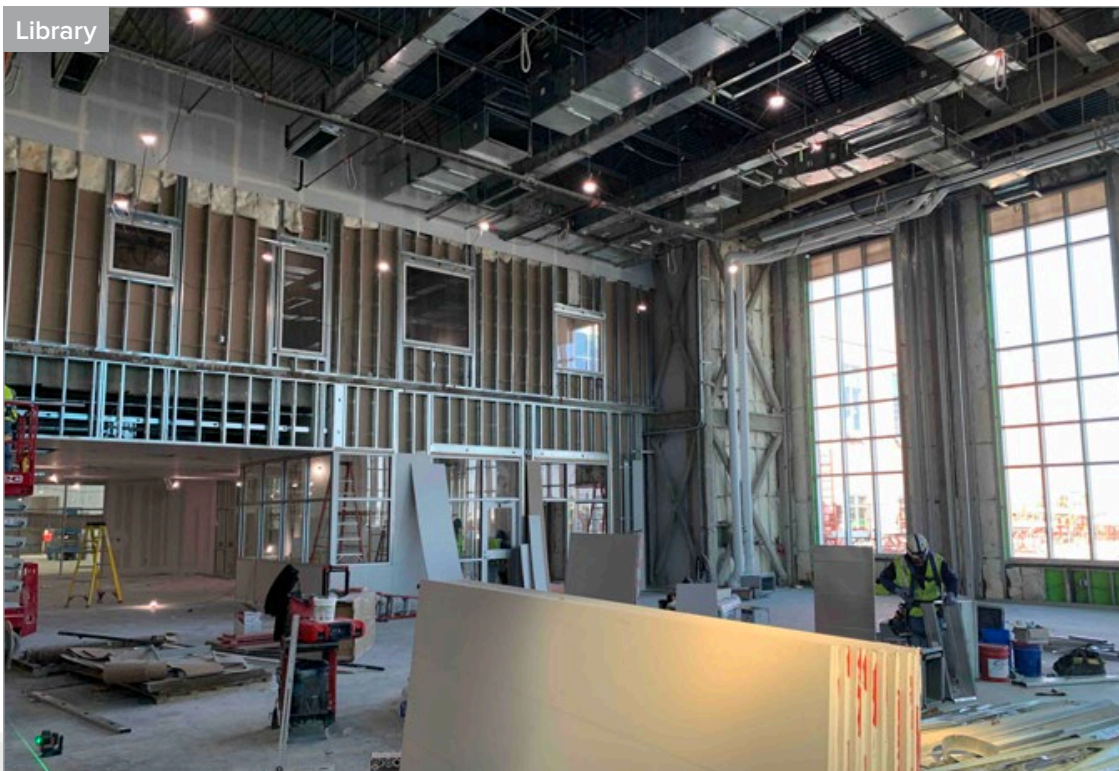

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2024

Library



Main Entry Corridor

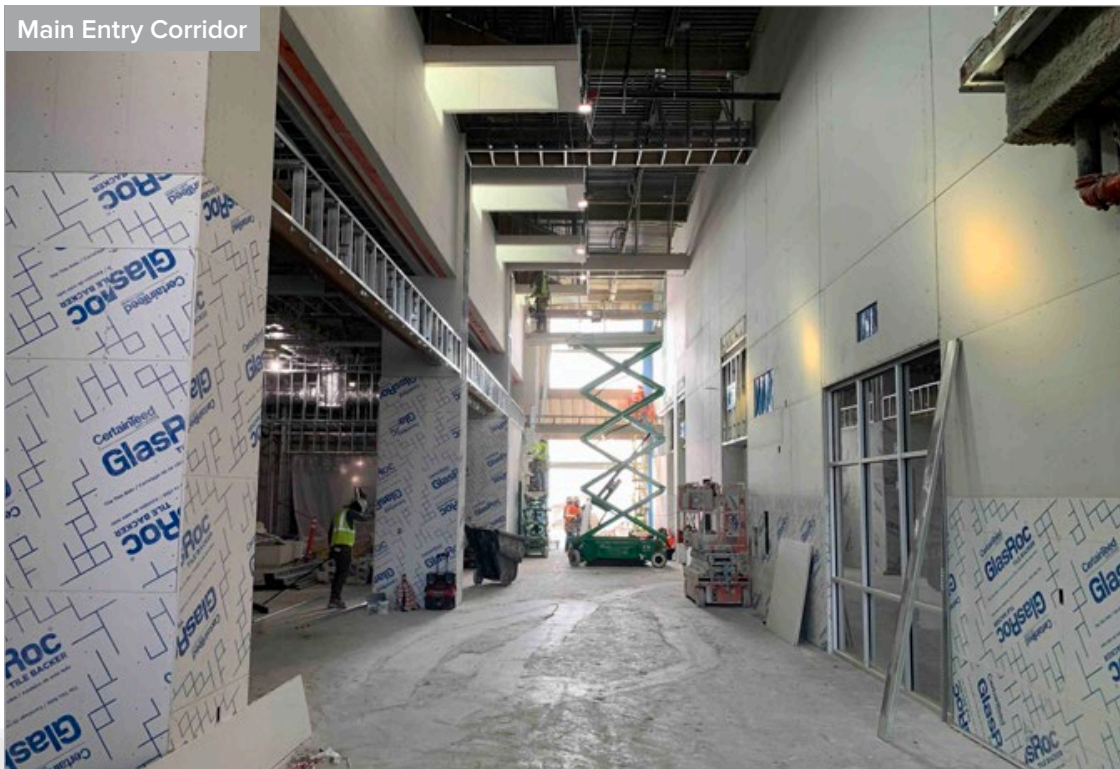

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2024

Student Commons



Student Commons

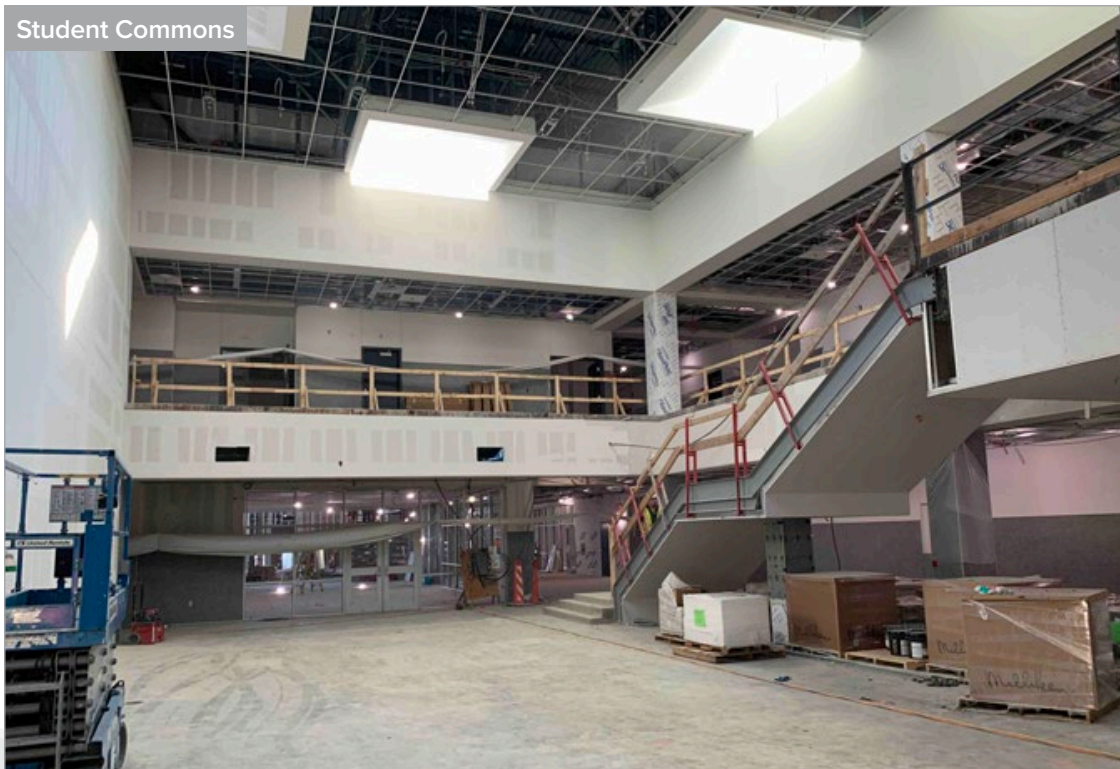

BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2024

Typical Casework Install

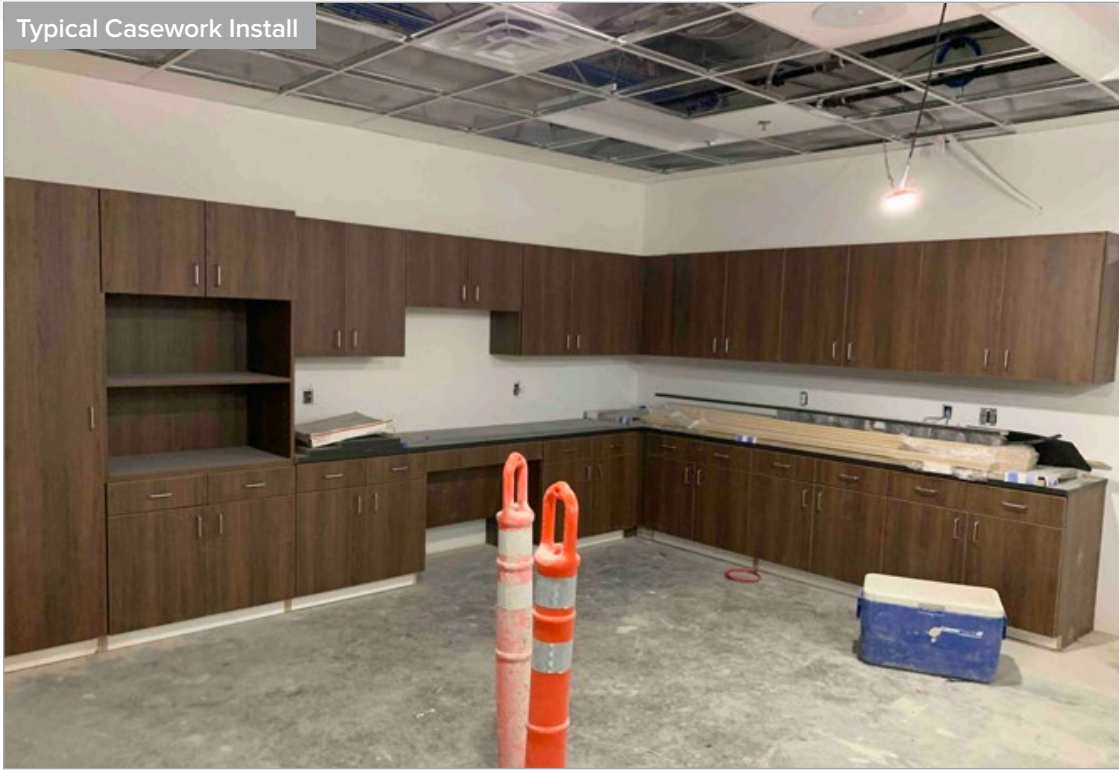

Science Classroom

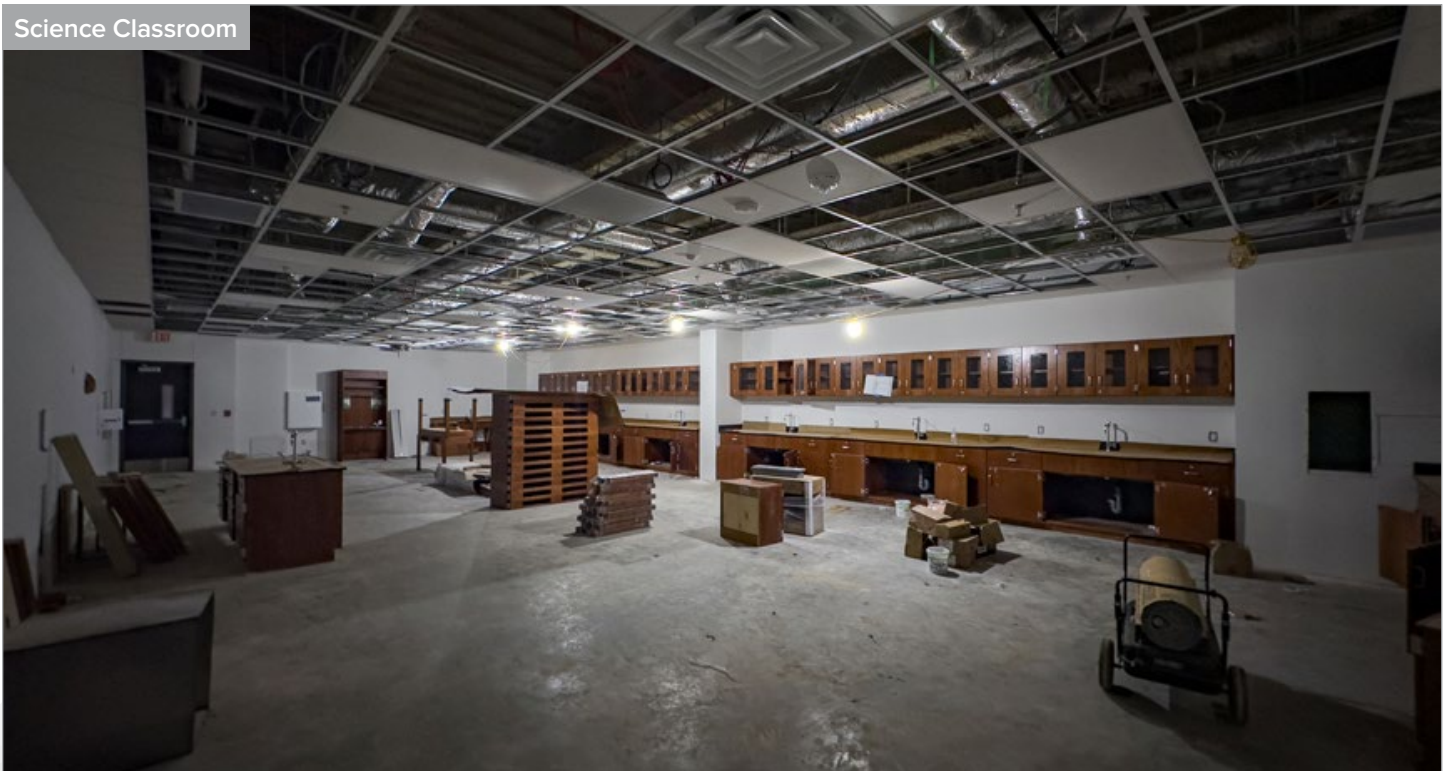

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2024

Multi-User Restroom



Academic Corridor

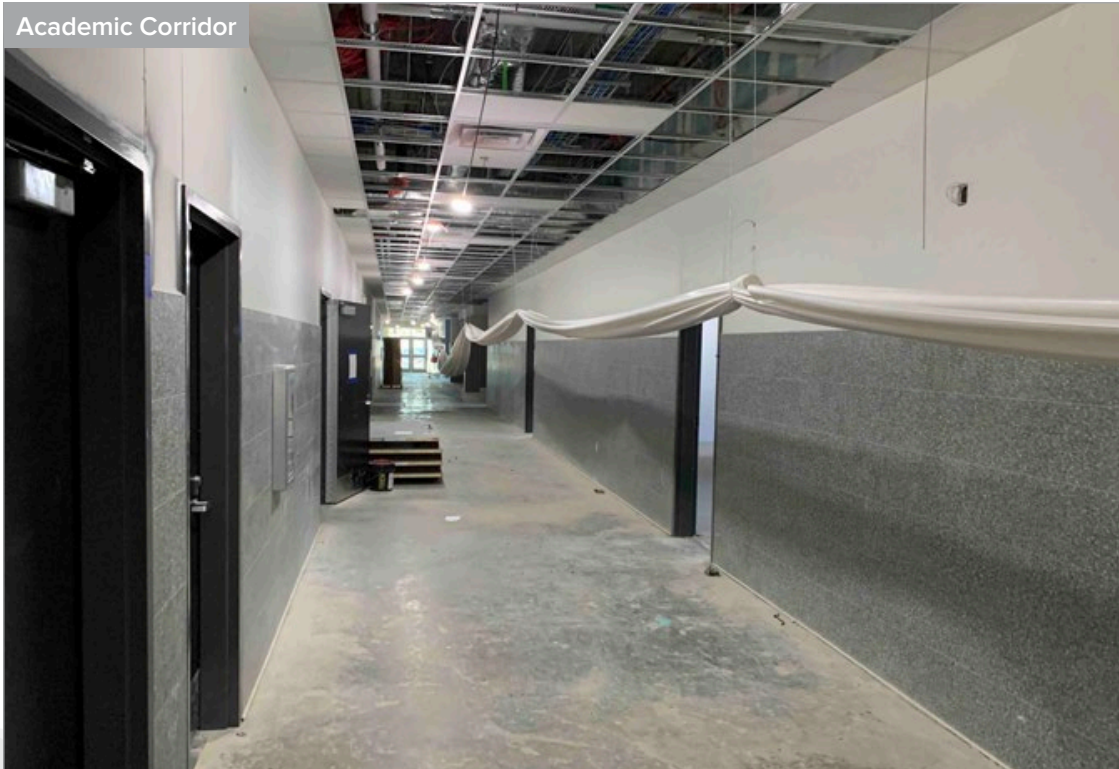

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2024

Storefront Install (Cafertorium)



Cafertorium Stage

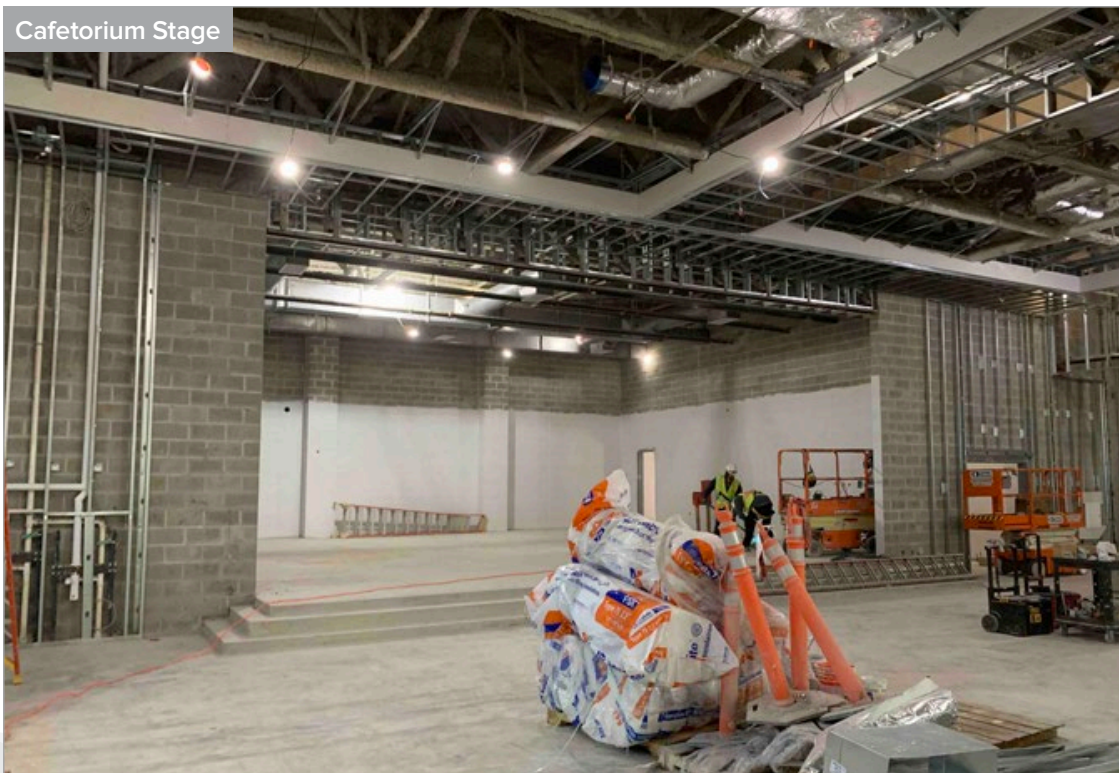


BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2024

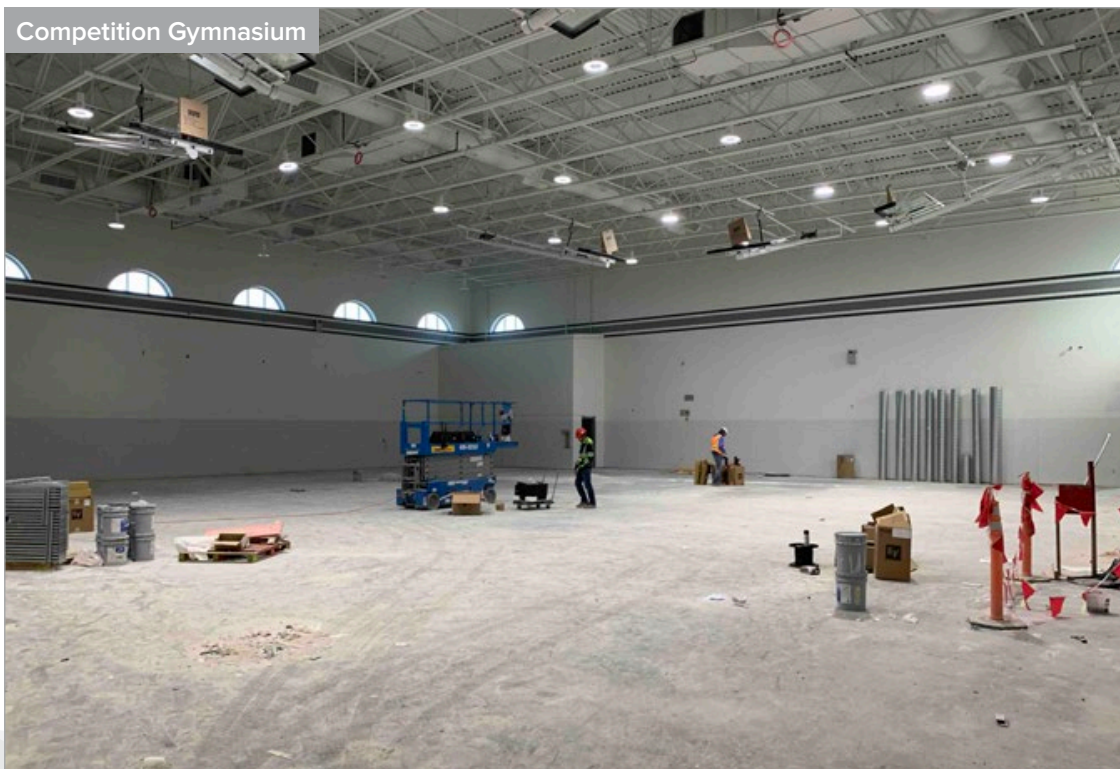

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2024

Auxiliary Gymnasium (Shelter)



Gymnasium Entry



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2024

Rear Entry



Rear Entry



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2024

Academic Wing Masonry Progress



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF FEBRUARY 2024

WORK COMPLETED AND ONGOING:

Site	Building
<ul style="list-style-type: none">• Fire lane paving complete• Drilling of irrigation water well will be complete this month• Drainage installation at the athletic field ongoing; followed by concrete curbs and asphalt at track• Concrete work associated with light pole bases will be complete this month• Site light poles will be installed this month• Musco light poles will be installed this month• Concrete work for tennis courts will begin this month• Concession stand foundation complete; access road to be complete this month	<ul style="list-style-type: none">• Structural steel erection ongoing at classroom area• Concrete roof at storm shelter will be placed this week• Slab over void forms will be placed in storm shelter as soon as weather allows• The second floor to be placed this week – Area 9• Fireproofing of structural steel will begin this week• Cold formed metal framing will begin at building exterior within the month• CMU masonry work ongoing – Areas 6 and 7• Installation of joists at competition gym will begin this week



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF FEBRUARY 2024



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF FEBRUARY 2024



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF FEBRUARY 2024

Piping and Duct Hangers



Academic Stair

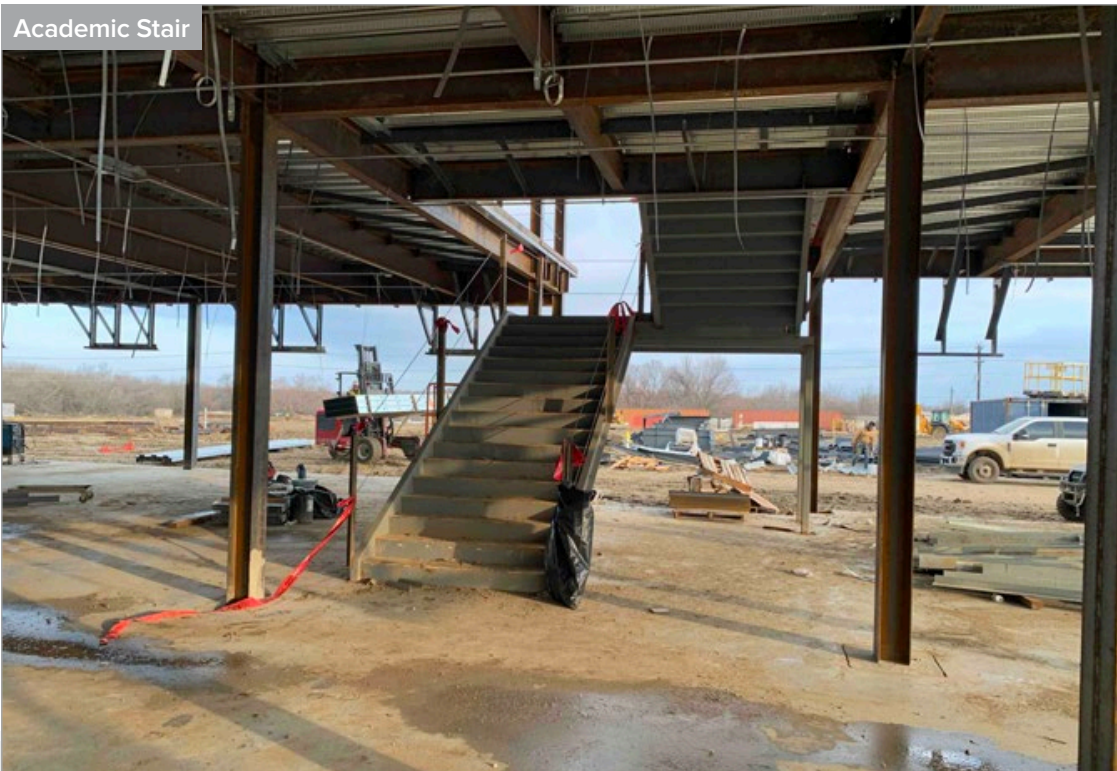

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF FEBRUARY 2024

Steel Decking (Second Floor)



Elevator Shaft



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF FEBRUARY 2024



Fine Arts/Athletics



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF FEBRUARY 2024

Auxiliary Gymnasium (Shelter)



Auxiliary Gymnasium (Shelter)



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF FEBRUARY 2024

CMU Block (Fine Arts)



Concession/Restroom Building



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF FEBRUARY 2024

Athletic Field/Track



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF FEBRUARY 2024

WORK COMPLETED AND ONGOING:

Site

- Remixing lime on south side of the building's fire lanes and parking lots
- Liming fire lanes around MPF building next week
- Gas line installation around MPF building ongoing
- Main electrical easement laid out; waiting on CoServ to begin the electrical underground installation
- CoServ has completed temporary power to job trailers and main building
- Grade beam forming and rough-in installation ongoing – Areas T and V; scheduled to pour those grade beams this week
- Moisture conditioning at tennis courts complete
- Moisture conditioning at baseball field beginning next week
- Pouring portions of south fire lanes and parking lots this week
- Prairie Drive utility installation ongoing

Building

- Grade beam installation ongoing – All Areas
- Slabs complete – Areas A, B, Q and R
- Grading is ongoing – Area C; planning to pour slab week of 2/12
- MEP underground complete – Areas A, B, C, Q, R and S; ongoing – Areas D, N and P
- Forming of concrete columns ongoing – Areas D and N; first column pours complete
- Steel erection ongoing – Area A; steel erection to begin next week – Area B
- Load bearing CMU wall installation ongoing – Areas Q and R



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF FEBRUARY 2024



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF FEBRUARY 2024



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




RICHLAND HIGH SCHOOL (HS #4)

AS OF FEBRUARY 2024

Student Commons (Steel Reinforcing for Concrete Columns)



Underslab Preparation for Void Box Placement

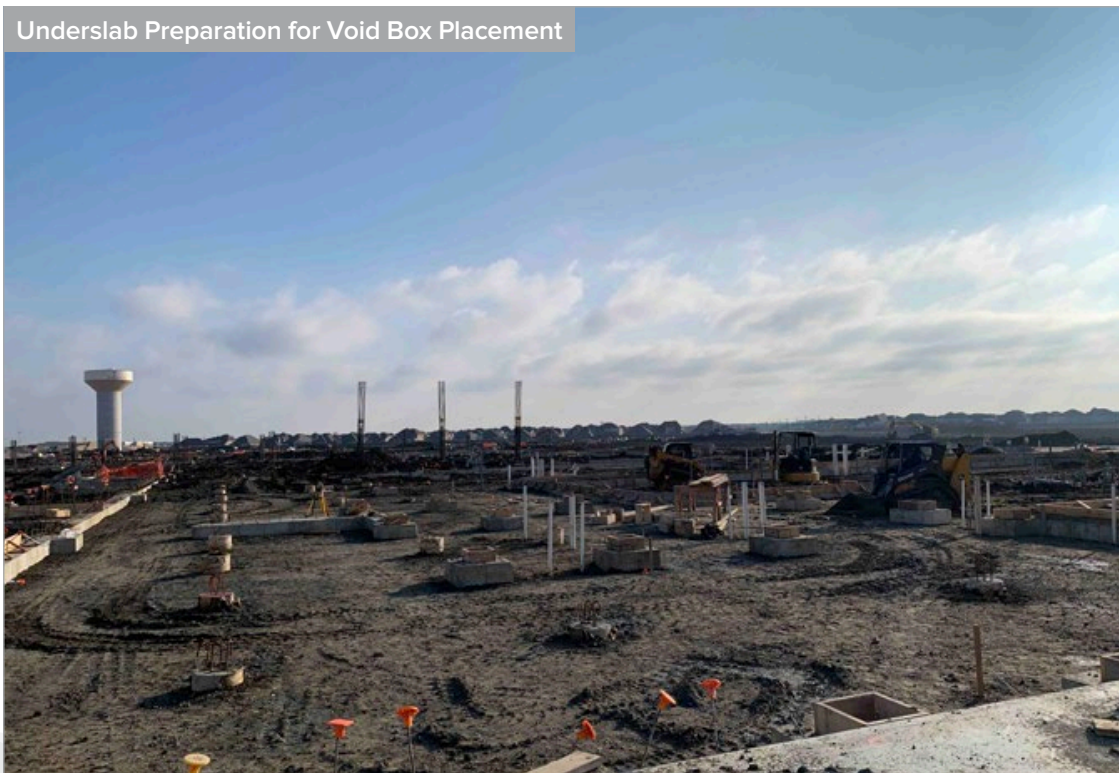

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF FEBRUARY 2024

West Academic Wing Steel Erection



Fine Arts Wing



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF FEBRUARY 2024

Auditorium



CMU Block (Fine Arts Wing)

