

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF NOVEMBER 2023

WORK COMPLETED AND ONGOING:

Site

- Paving is 90% complete
- Lime stabilization ongoing
- Irrigation installation to begin end of November

Building

- Building slab complete – Areas 3 and 4; Area 2 to pour first week of November
- Precast concrete panel installation upcoming at tornado shelter
- ICF installation ongoing



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF NOVEMBER 2023



LOOKING EAST

Betty Jackson Elementary School



LOOKING SOUTH

Betty Jackson Elementary School

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF NOVEMBER 2023



LOOKING WEST

Betty Jackson Elementary School

ICF Installation



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF NOVEMBER 2023

Tornado Shelter Foundation Prep



ICF Installation



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF NOVEMBER 2023

Foundation Prep - Area 2



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF NOVEMBER 2023

WORK COMPLETED AND ONGOING:

Site

- Football field subgrade prep ongoing
- Trench drain installation at football field ongoing
- Sidewalk installation along Prestwick ongoing
- Masonry veneer at pump house ongoing
- Flume installation in the West detention pond complete
- Light pole installation complete
- Concession stand masonry veneer is 90% complete
- Final grading and topsoil installation ongoing

Building

- Exterior sheathing near complete – Areas 1, 2, 3, 9, 10 and 11
- Storefront window installation ongoing – Areas 1, 2, 3, 9, 10 and 11
- MEP rough-in ongoing
- Interior wall framing ongoing – Areas 9, 10 and 11
- One-siding sheetrock – Areas 2, 3, 10, and 11
- Two-siding sheetrock – Areas 1 and 9
- Tile installation ongoing in multi-user restrooms and academic corridors
- Steel erection ongoing – Areas 4, 5, 7 and 8
- CMU installation ongoing – Areas 4, 5, 6 and 7
- Tornado Shelter MEP rough-in ongoing
- Air barrier installation ongoing – Area 4
- Exterior masonry veneer ongoing – Areas 5, 6 and 7
- Roofing ongoing – Areas 5, 6, 7, 9, 10 and 11



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF NOVEMBER 2023



LOOKING EAST

Daniel L. Jones Middle School



LOOKING SOUTH

Daniel L. Jones Middle School

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF NOVEMBER 2023



LOOKING WEST
Daniel L. Jones Middle School

Exterior Masonry Progress



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF NOVEMBER 2023

Exterior Masonry Progress



Gymnasium Entry



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF NOVEMBER 2023

Main Entry Corridor



Library



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF NOVEMBER 2023

Cafetorium



Student Commons Stair

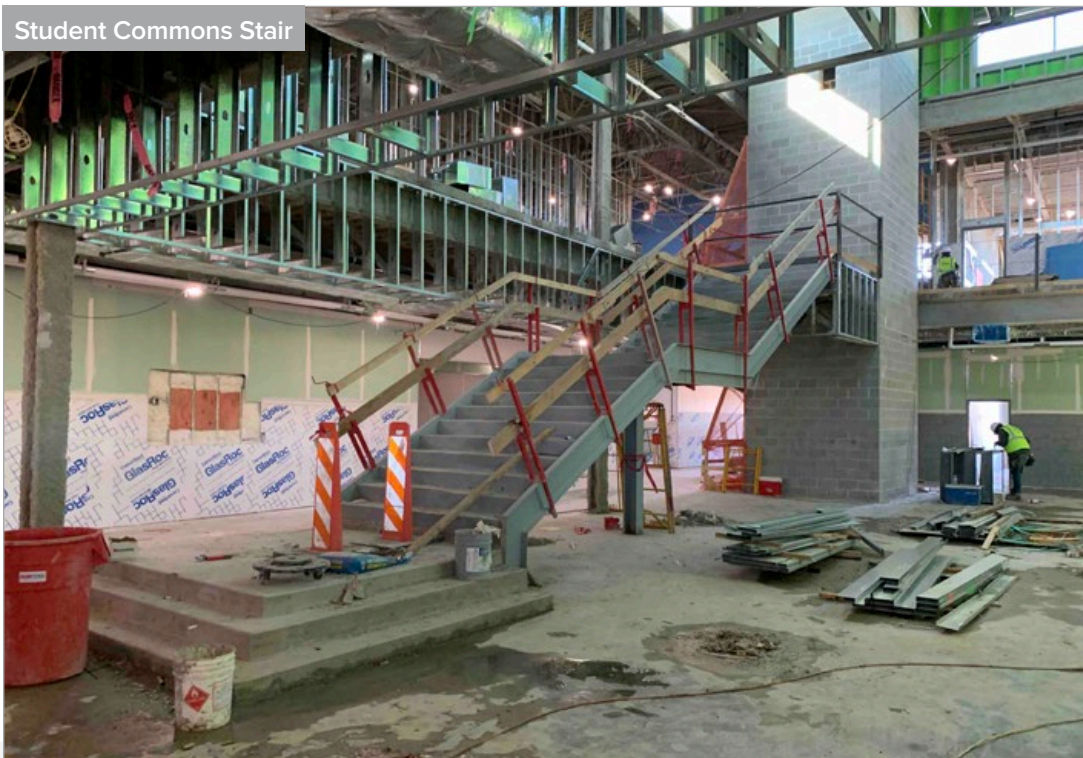

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF NOVEMBER 2023

Student Commons



Academic Corridor

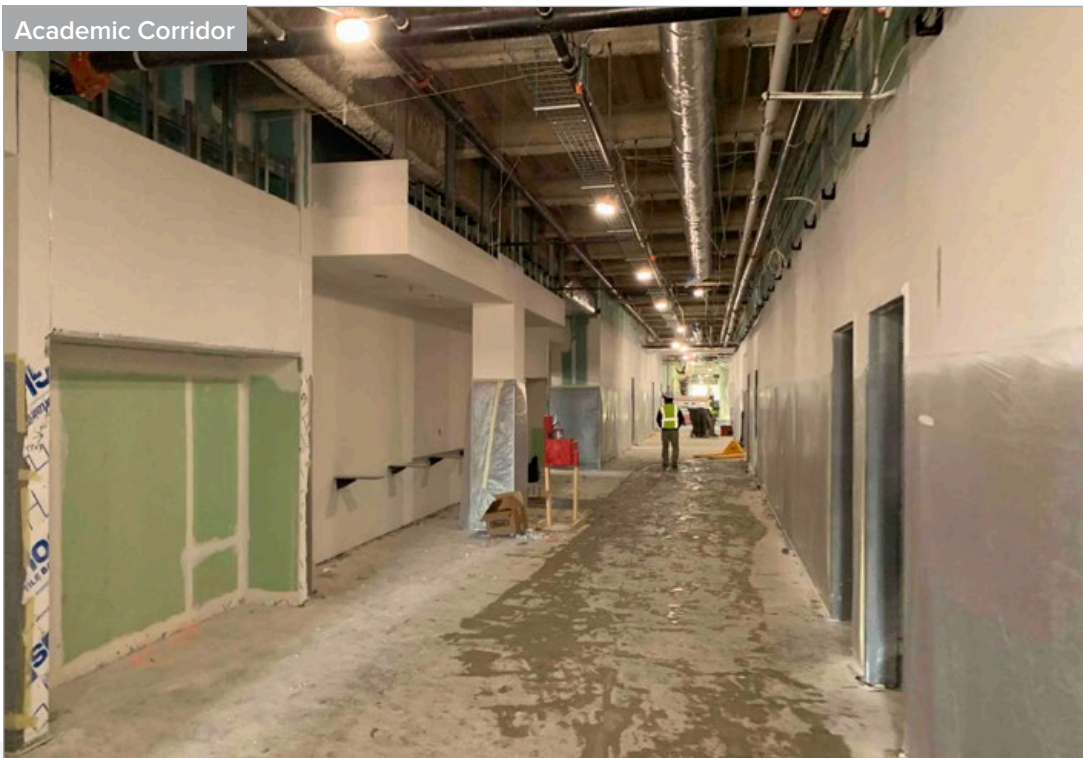

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF NOVEMBER 2023

Multi-User Restroom



Academic Wing Exterior Progress




BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF NOVEMBER 2023

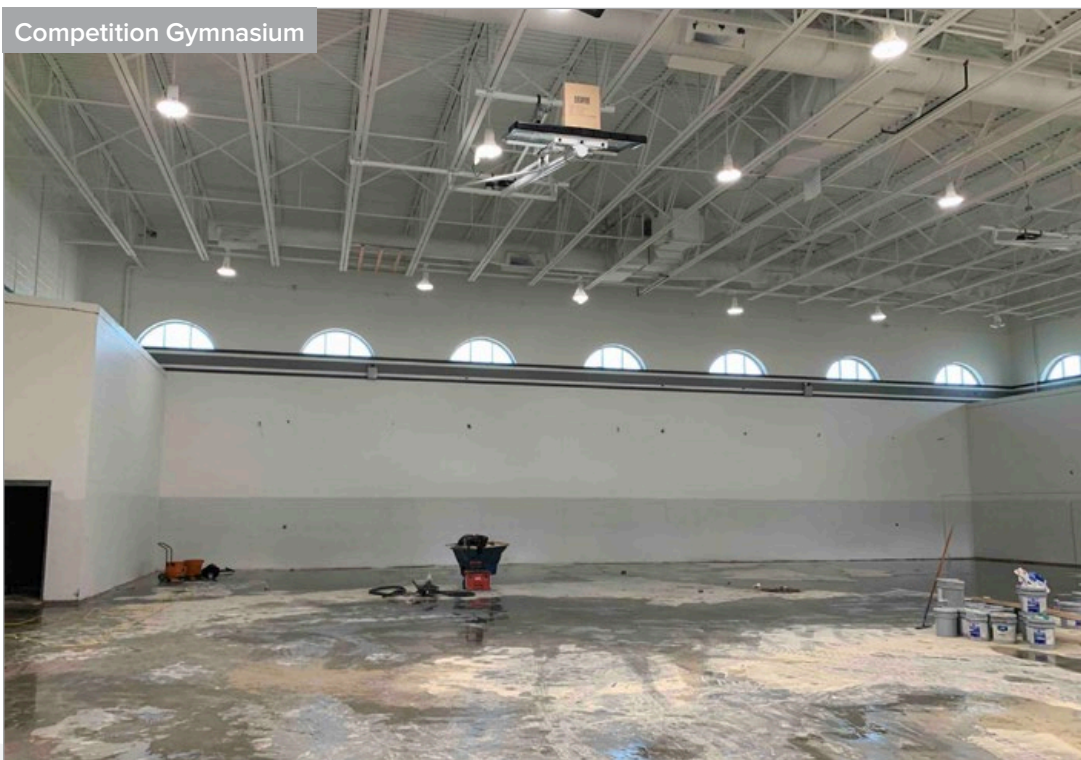

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF NOVEMBER 2023

Secondary Gymnasium (Tornado Shelter)



Concrete Locker Bases (Locker Rooms)

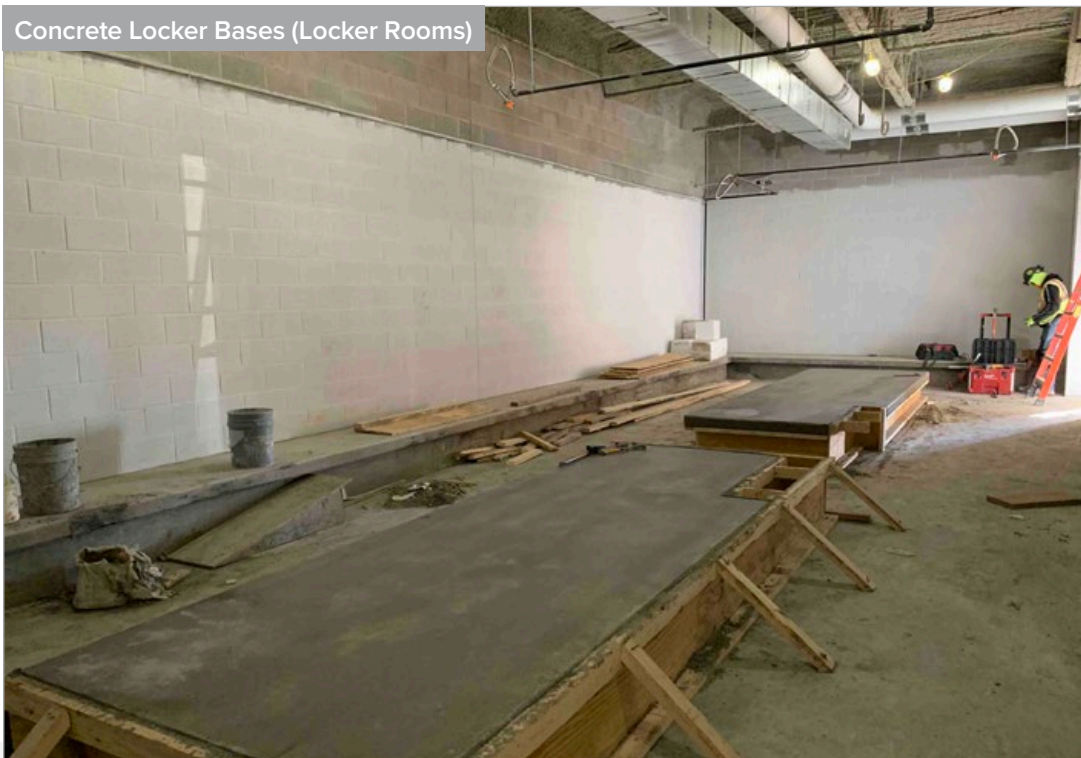

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF NOVEMBER 2023

Athletic Field Concession/Restroom Building



Athletic Field Progress



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF NOVEMBER 2023

WORK COMPLETED AND ONGOING:

Site

- Field contractor has finished moisture conditioning track in its entirety; currently moisture conditioning field
- Auger Cast Piles have been drilled for concession building, pump house, and marquee sign
- Water Line 'A' installed up to Teel Pkwy and hydro tested
- Storm Drain Line 'B' installation ongoing
- Storm Drain Line 'C' is completely installed
- Sanitary Line is installed around the building, aside from where it goes towards the west of the property for tie in
- Subgrade preparation for paving at the east elevation complete and ready for lime stabilization
- Irrigation sleeves and site electrical underground installed at the east elevation for lime stabilization

Building

- Grade beams complete – Areas 1,2,3,5,6 and 7
- Underground utilities complete – Area 1 and 7
- Backfill process for grade beams ongoing and placing slab forms ongoing – Areas 1 and 7; will begin the fine grading process as soon as the weather allows
- Underground plumbing complete – Areas 5 and 6; ongoing – Area 2
- Underground for electrical complete – Areas 3 and 8; ongoing – Area 2
- The elevator pit is poured and ready to receive waterproofing



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF NOVEMBER 2023



LOOKING EAST
W. H. Moseley Middle School



LOOKING SOUTH
W. H. Moseley Middle School

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF NOVEMBER 2023



LOOKING WEST
W. H. Moseley Middle School

Firelane Subgrade Prep

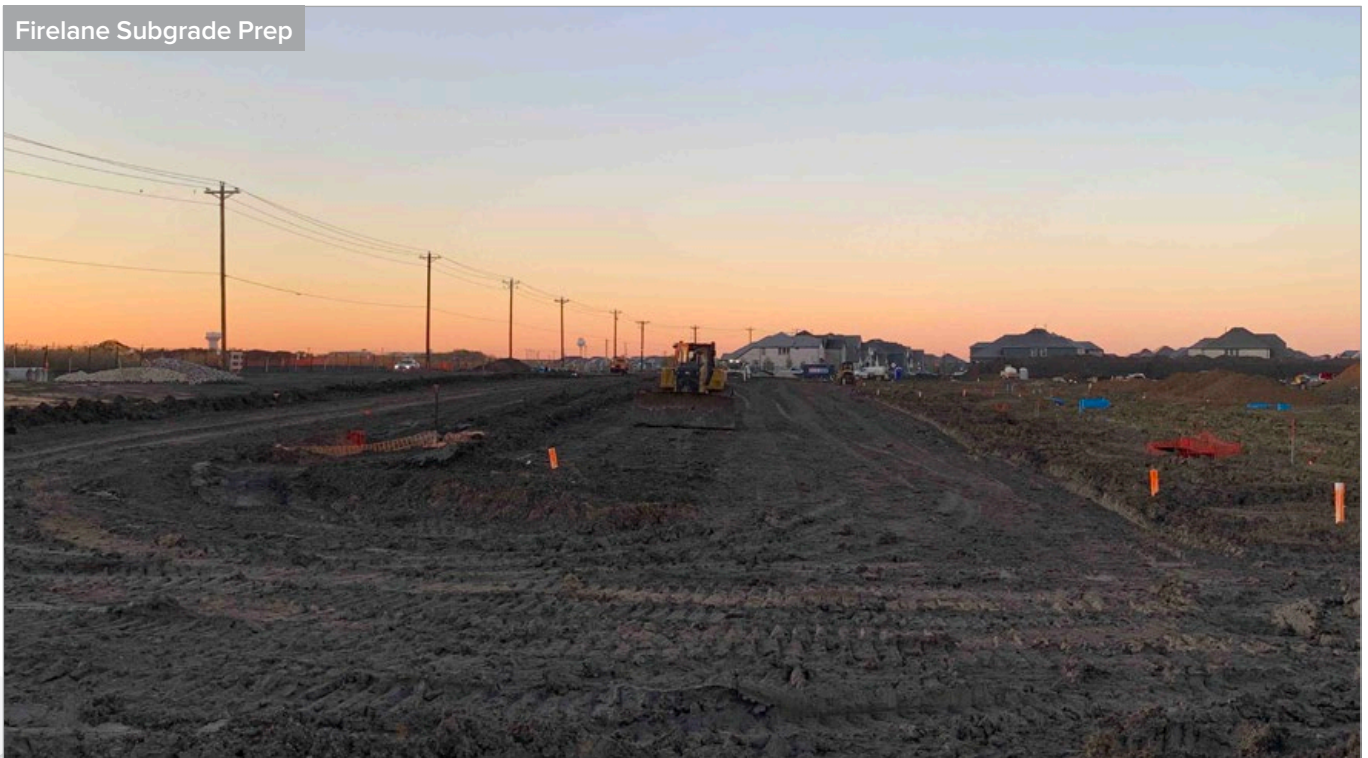

BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF NOVEMBER 2023

Underground Site Utility Installation

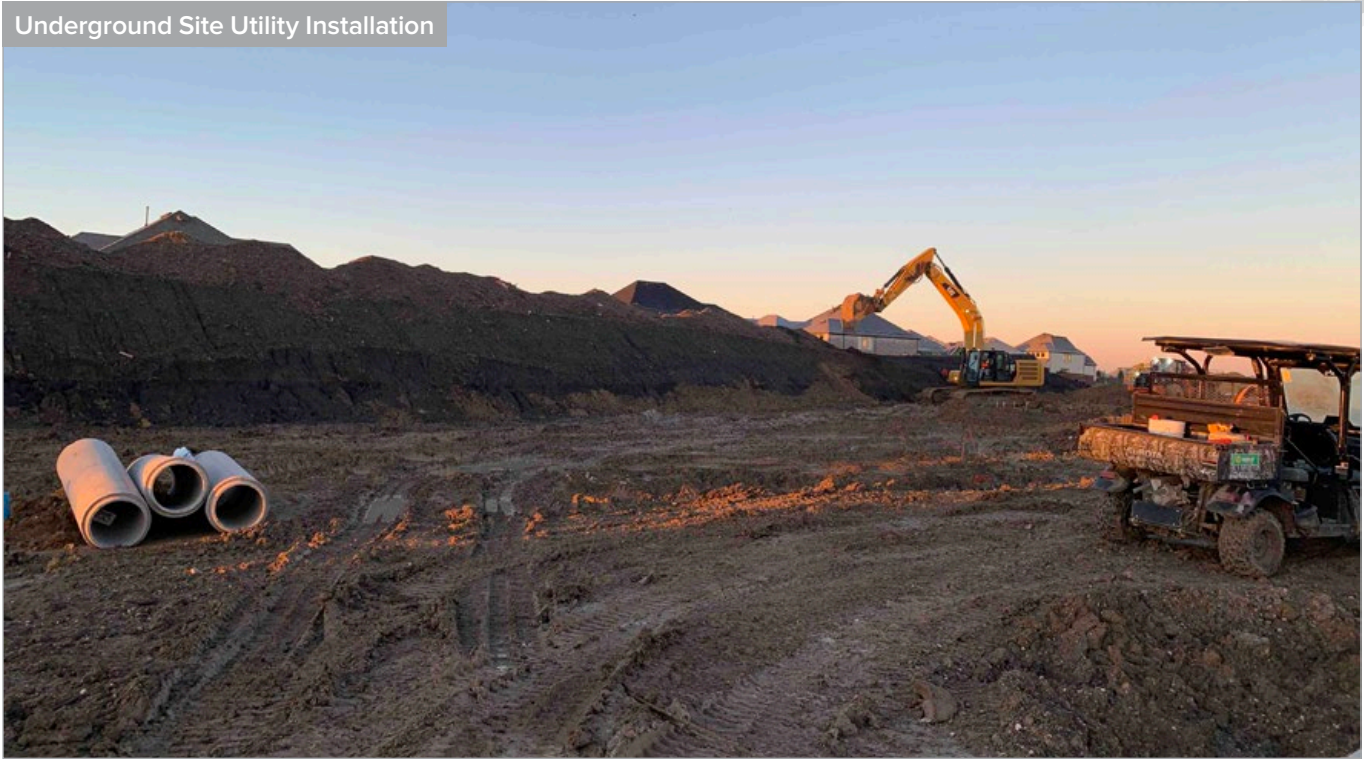

Grade Beam Backfilling



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF NOVEMBER 2023

Grade Beam Backfilling



Grade Beam Backfilling



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF NOVEMBER 2023

Formwork for Foundation Placement



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF NOVEMBER 2023

WORK COMPLETED AND ONGOING:

Site

- Final subgrade elevation checks on north parking lot complete
- Pouring remainder of north parking lot as soon as weather allows
- Storm Drain Lines F and G complete
- Storm Drain Lines A, C and D 50% complete
- Water Line D complete
- Water Lines A, B and C ongoing
- Sanitary Sewer Lines A and D complete
- Sanitary Sewer Line B ongoing
- Installation of irrigation sleeves and underground electrical to light poles in the south parking lots ongoing
- Liming of north fire lane to begin as soon as weather permits
- Gas line installation ongoing
- Light pole base installation in parking lots ongoing

Building

- Auger Cast Piles complete – Areas A, B, C, D, P, Q, R, S and N
- Auger Cast Piles ongoing – Areas E, J and M
- Grade beams complete – Areas A, B, P and R
- Grade beam installation ongoing – Areas C, D, Q and S
- MEP underground ongoing – Area A
- Building permit was released 10/19/2023



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF NOVEMBER 2023




BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




RICHLAND HIGH SCHOOL (HS #4)

AS OF NOVEMBER 2023

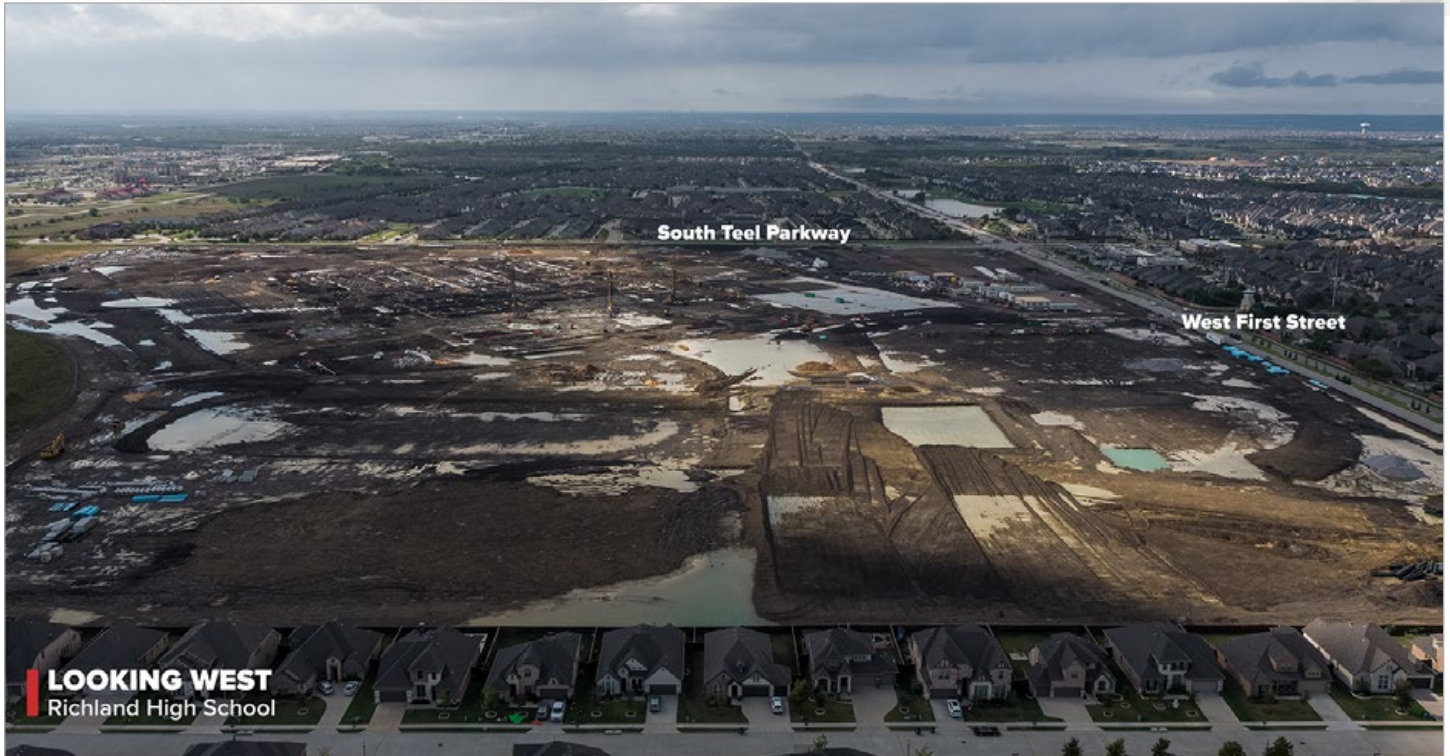

Auger Cast Pile Installation

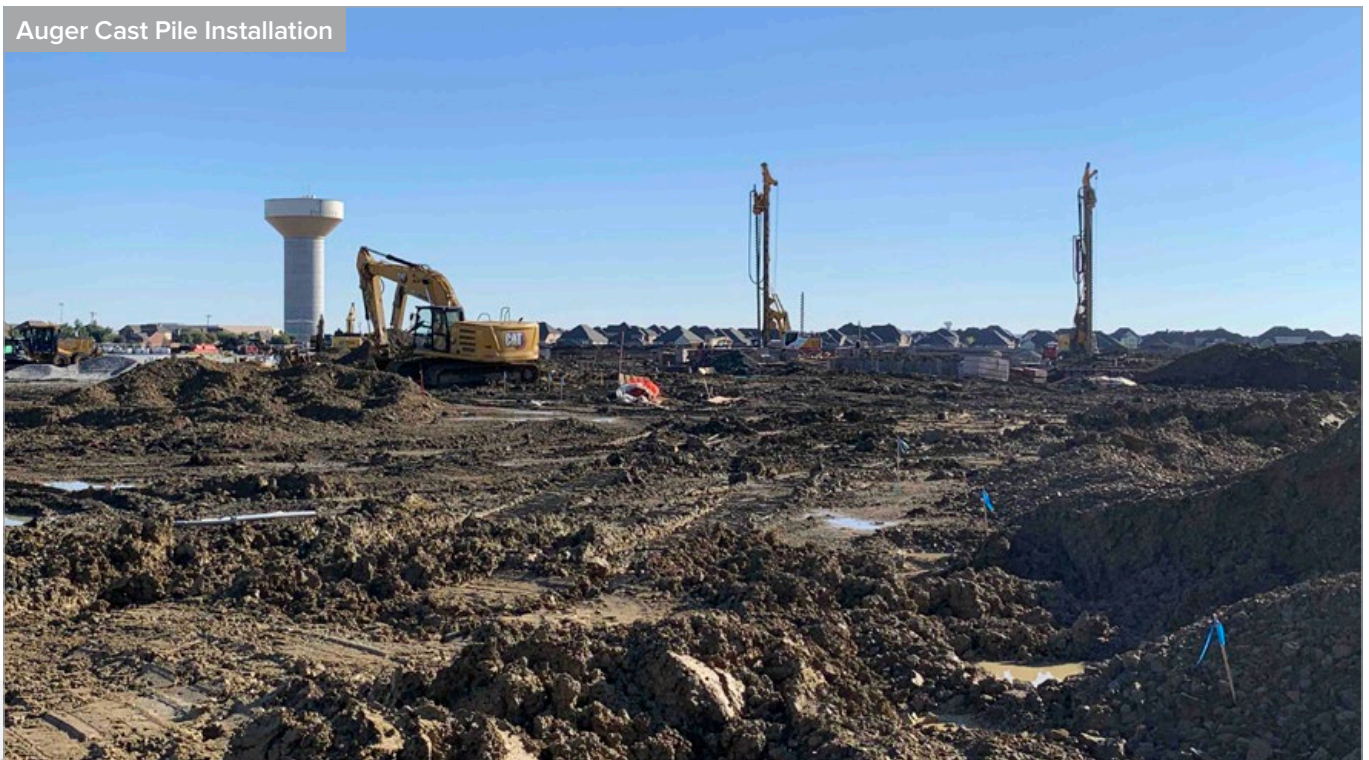

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF NOVEMBER 2023

Grade Beam Reinforcing



Grade Beam Formwork



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF NOVEMBER 2023

Grade Beam Formwork



Grade Beam Formwork



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF NOVEMBER 2023

Complete Grade Beam



Complete Grade Beam

