

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF MARCH 2024

WORK COMPLETED AND ONGOING:

Site

- Alvira Drive and Cassidy Street paving ongoing
- Prepping subgrade for flat work around tornado shelter and playground areas
- Irrigation is 95% complete; sod and tree installation ongoing

Building

- Exterior brick around shelter and above roof at cafeteria complete
- Brick installation ongoing along north side – Areas 1, 2 and 3
- All areas are dried in; white cap installation ongoing
- Kitchen floor and wall tile installation ongoing
- Tape and bed in cafeteria and admin ongoing
- Painting in tornado shelter ongoing
- All main corridor furr-downs complete; tape and bed ongoing
- Cold formed metal framing (CFMF) ongoing – Area 1
- Drywall complete – Area 3
- RTU installation complete



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF MARCH 2024



LOOKING EAST

Betty Jackson Elementary School



LOOKING SOUTH

Betty Jackson Elementary School

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF MARCH 2024



Exterior Masonry Progress



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF MARCH 2024



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF MARCH 2024

Main Entry Corridor



Academic Corridor

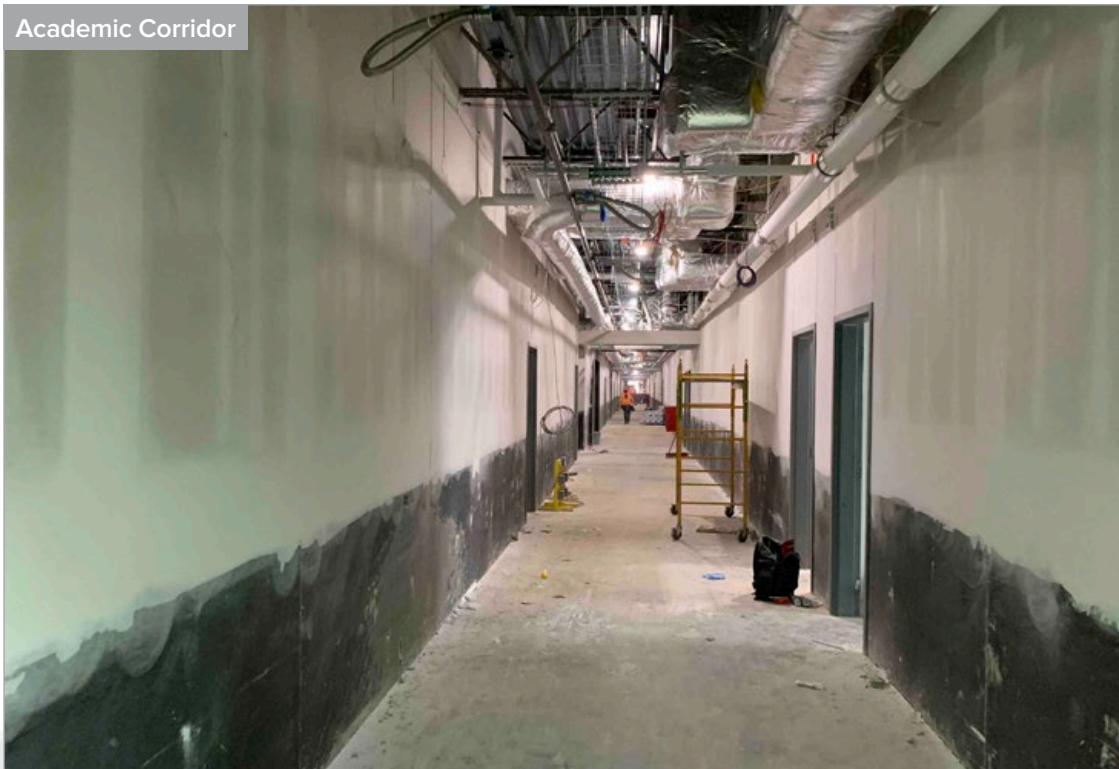


BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF MARCH 2024

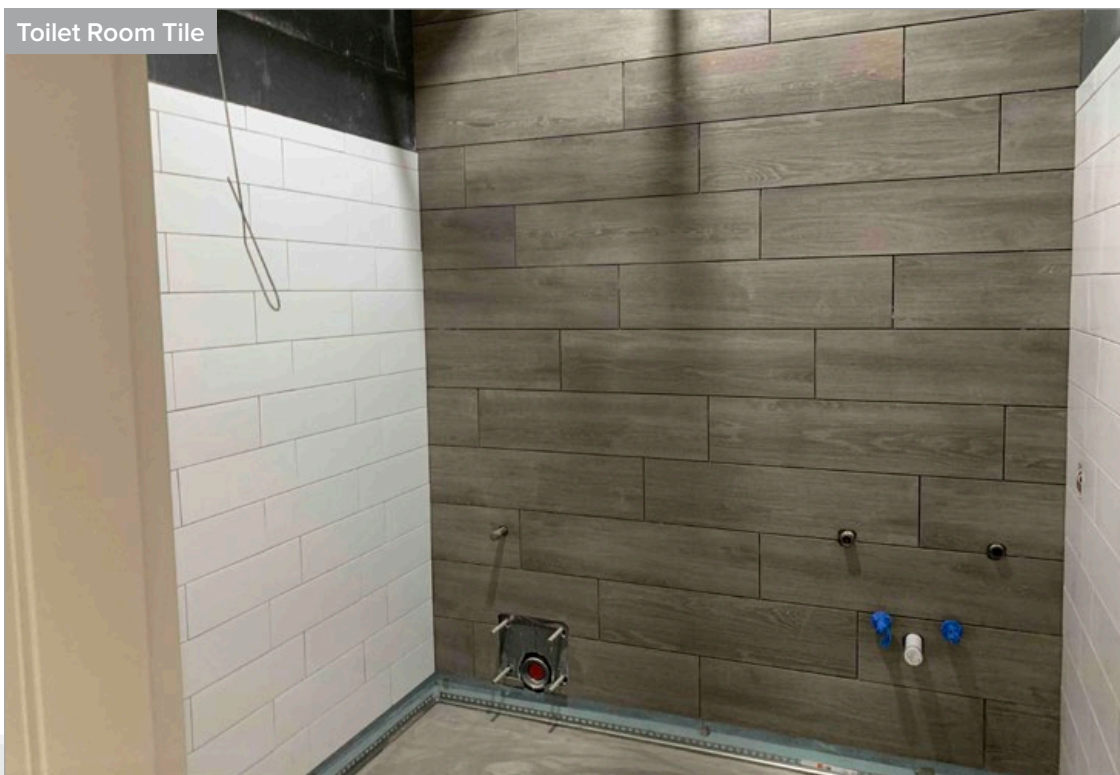



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF MARCH 2024

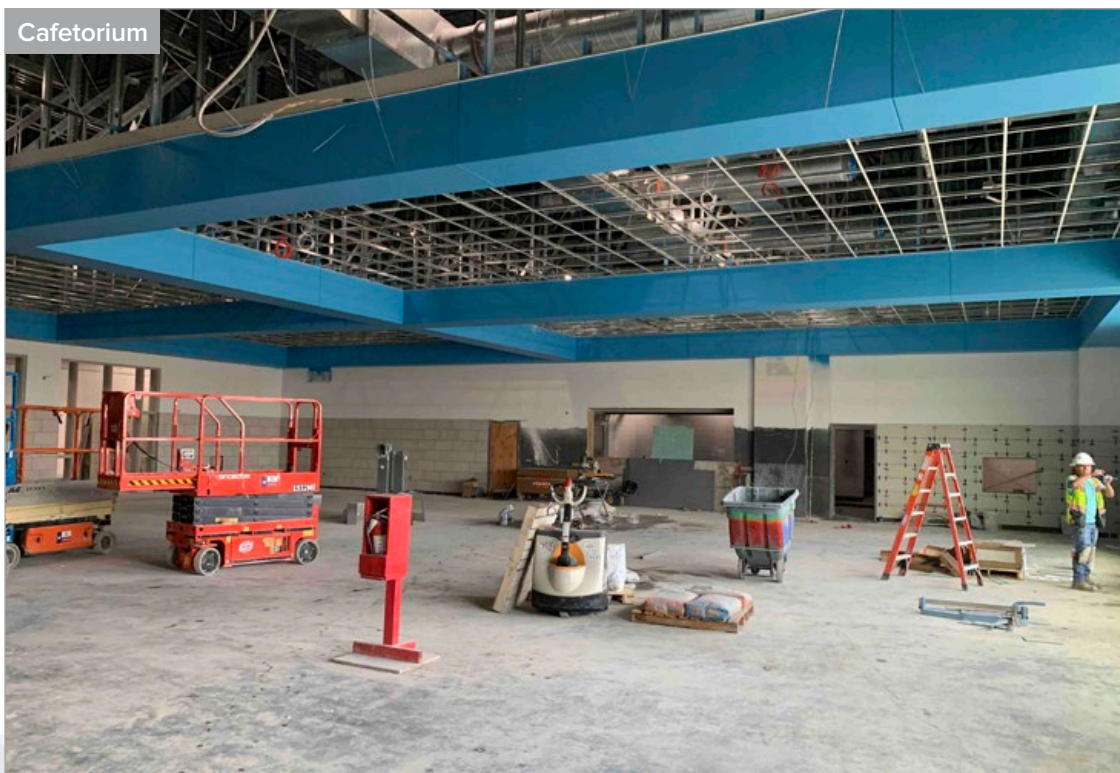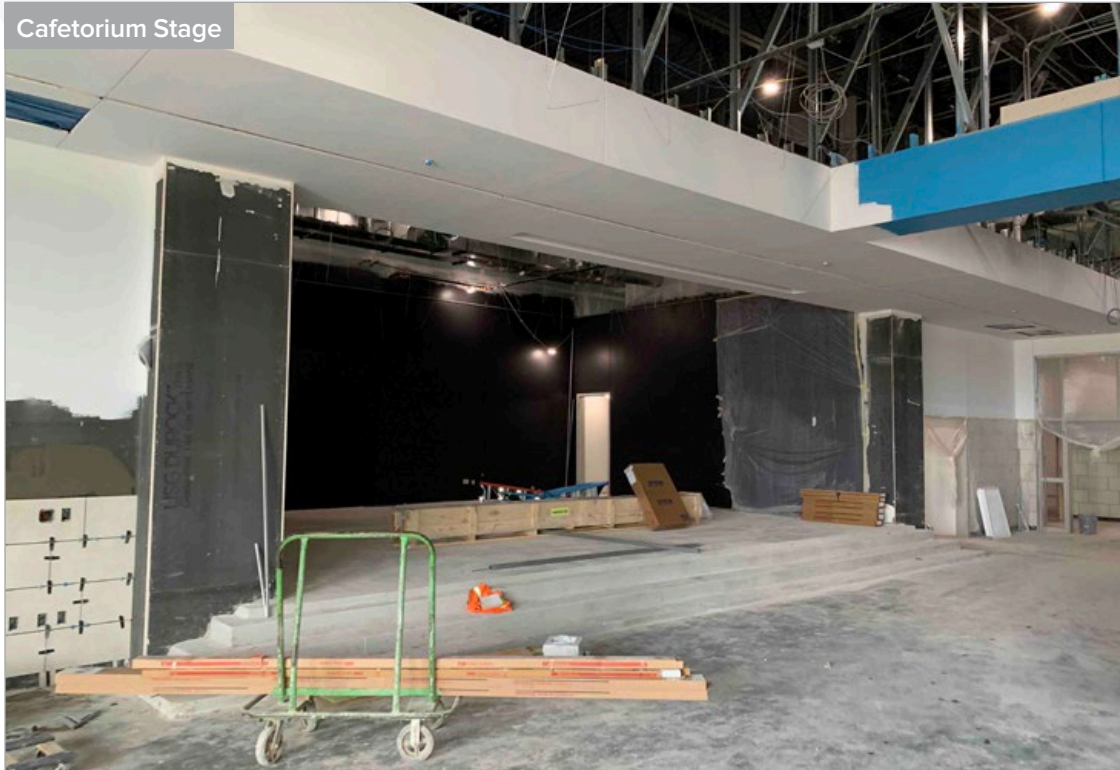


BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF MARCH 2024

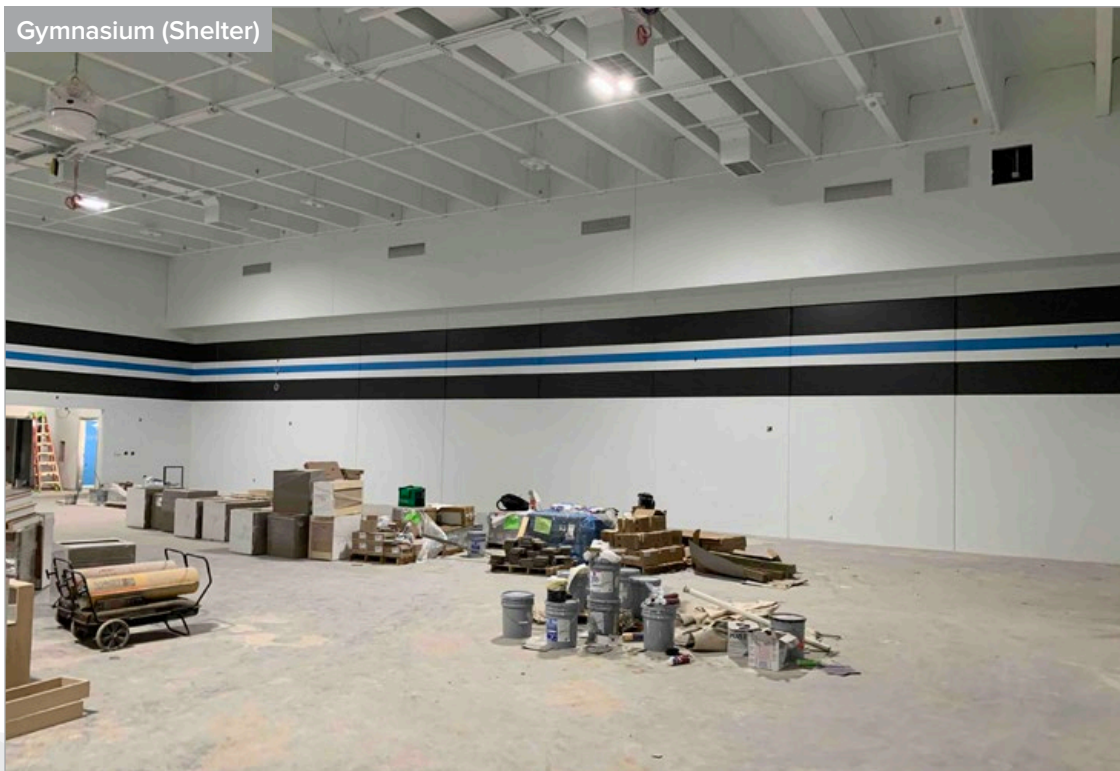

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF MARCH 2024



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF MARCH 2024

WORK COMPLETED AND ONGOING:

Site

- Football field subgrade prep complete.
- Track asphalt poured; track markings and turf installation this month
- Track and football field flatwork ongoing
- Field events equipment ongoing
- Tennis court fencing complete
- Tennis court flatwork and bleachers installation complete
- Sidewalk installation along Hardy Drive ongoing
- Pump house and concession stand veneer and roof complete
- Final grading and topsoil installation ongoing
- Irrigation installation ongoing
- Decorative metal fence installation ongoing
- Irrigation tank installation ongoing

Building

- Exterior sheathing and weather barrier installation complete
- Storefront window installation complete
- MEP rough-in ongoing – All Areas
- MEP and Technology inspections complete – Areas 1-3, 9-11; Areas 5-7 upcoming
- Gas and electric meters hooked up and functioning
- Roof-top unit (RTU) start-up ongoing – Academic wing
- Interior wall framing ongoing – Area 8
- Two-siding of sheetrock complete – Area 8
- Tape, bed and paint ongoing – Areas 7-11
- Tile installation ongoing in multi-user restrooms and academic corridors
- Classroom carpet and millwork installation ongoing
- Science lab casework installation ongoing
- Tornado shelter MEP rough-in ongoing
- Exterior veneer ongoing – Areas 8-11
- Roofing ongoing – Area 8; installation complete – Areas 1-7, and 9-11



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF MARCH 2024



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF MARCH 2024



Main Entry



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF MARCH 2024

Main Entry Corridor



Library Windows

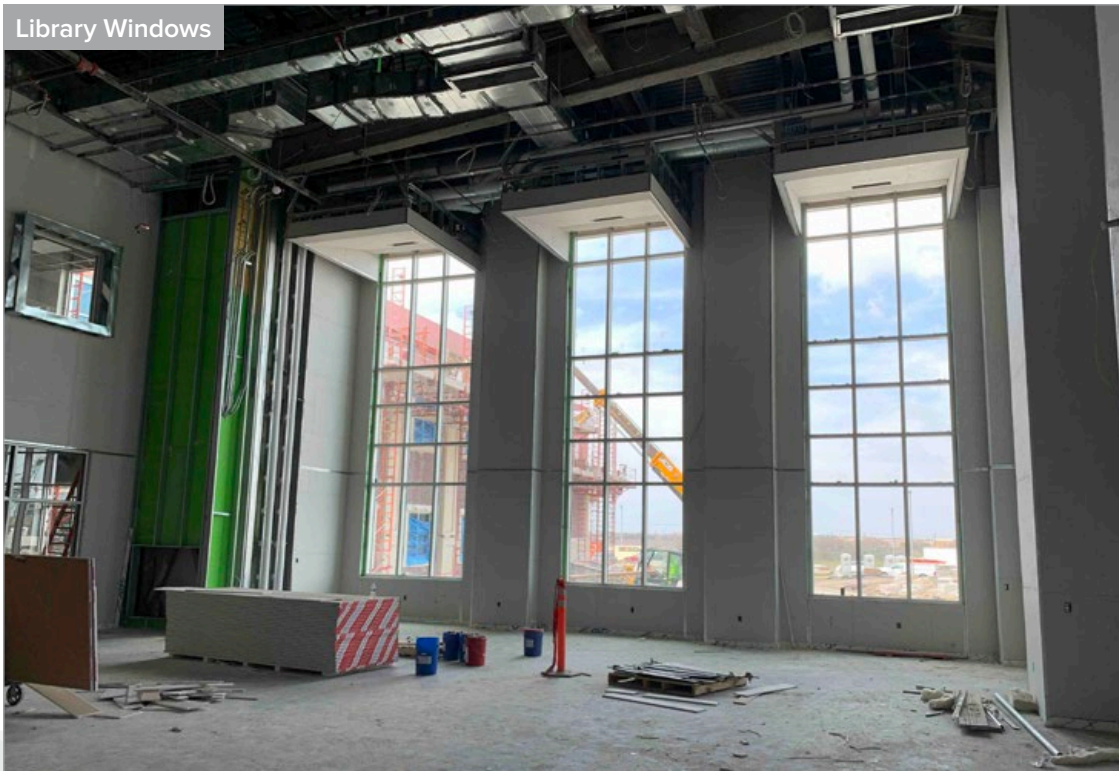

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF MARCH 2024

Library



Student Commons

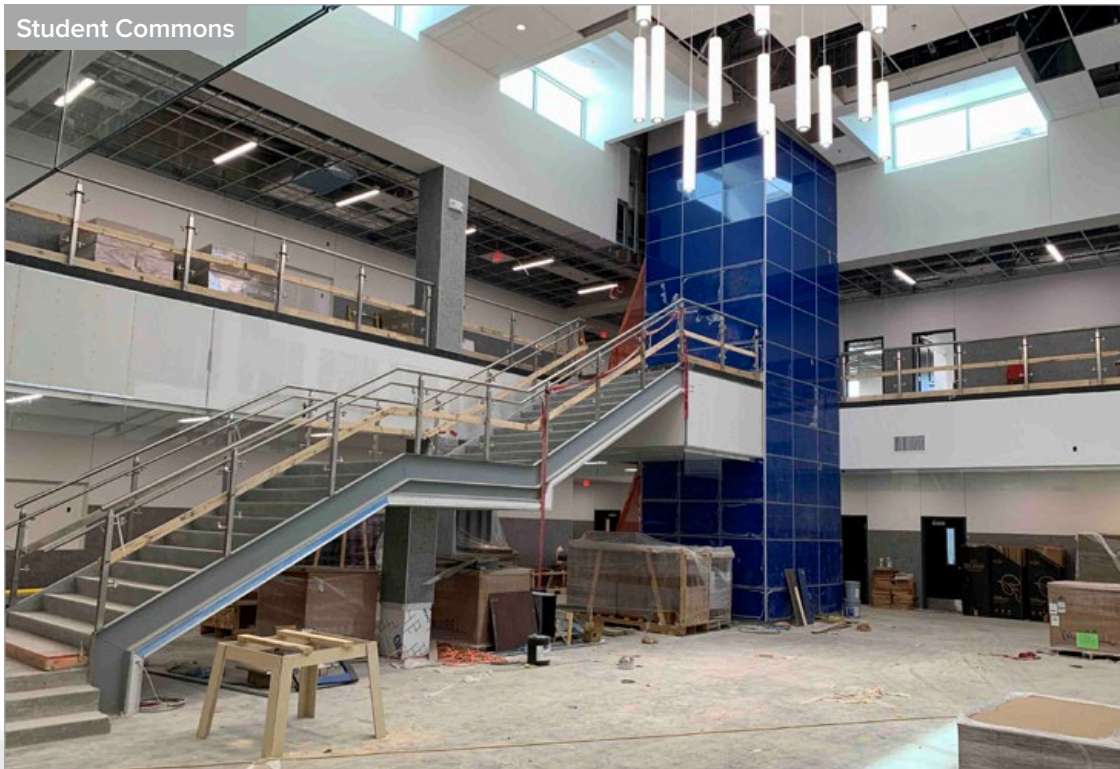

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF MARCH 2024

Academic Corridor



Academic Corridor

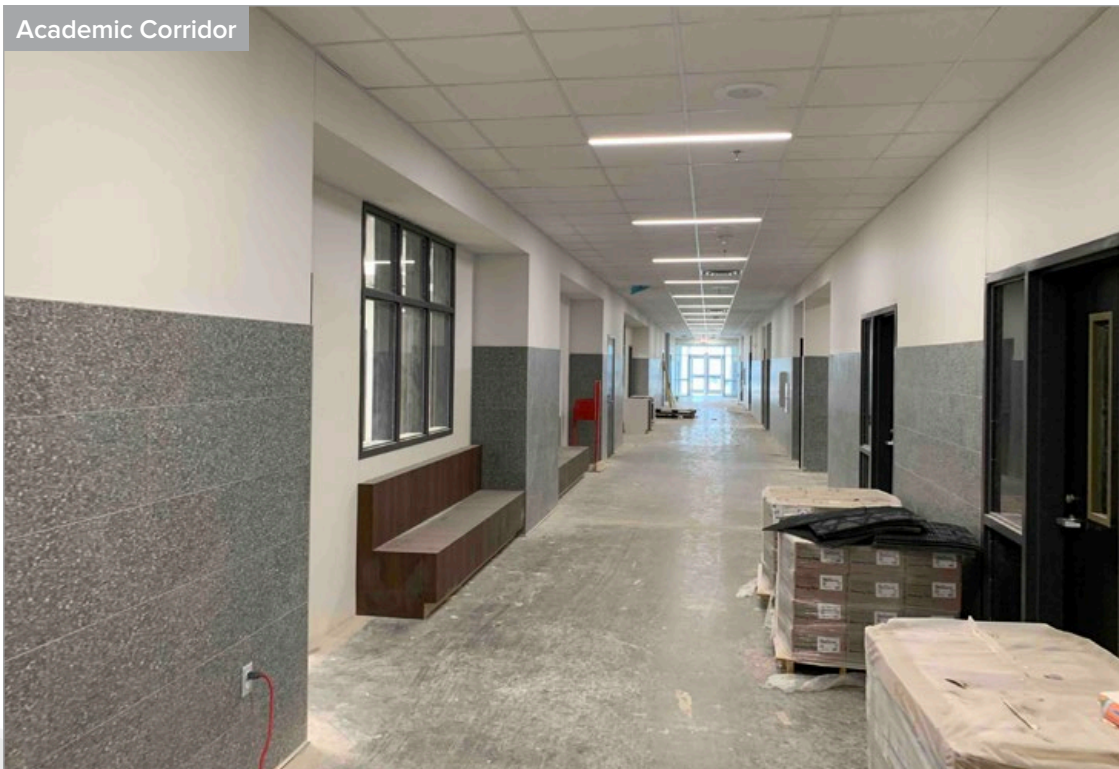

BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF MARCH 2024

Multi-User Restroom

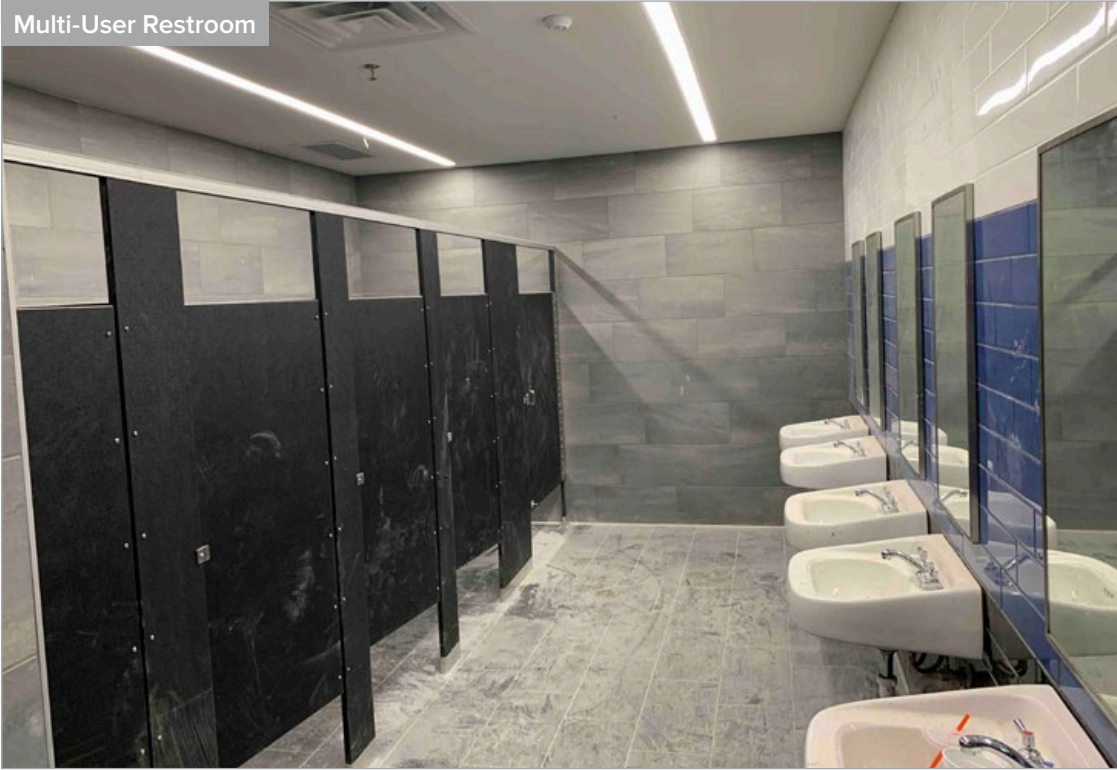

Science Classroom

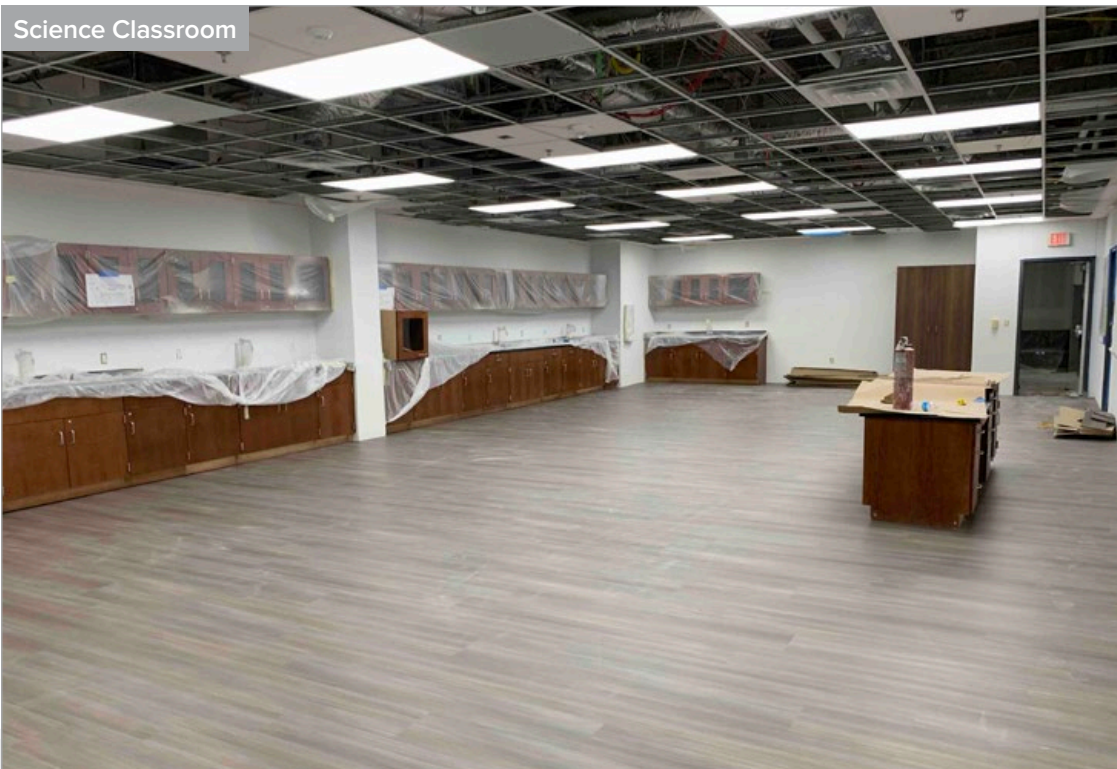


BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF MARCH 2024

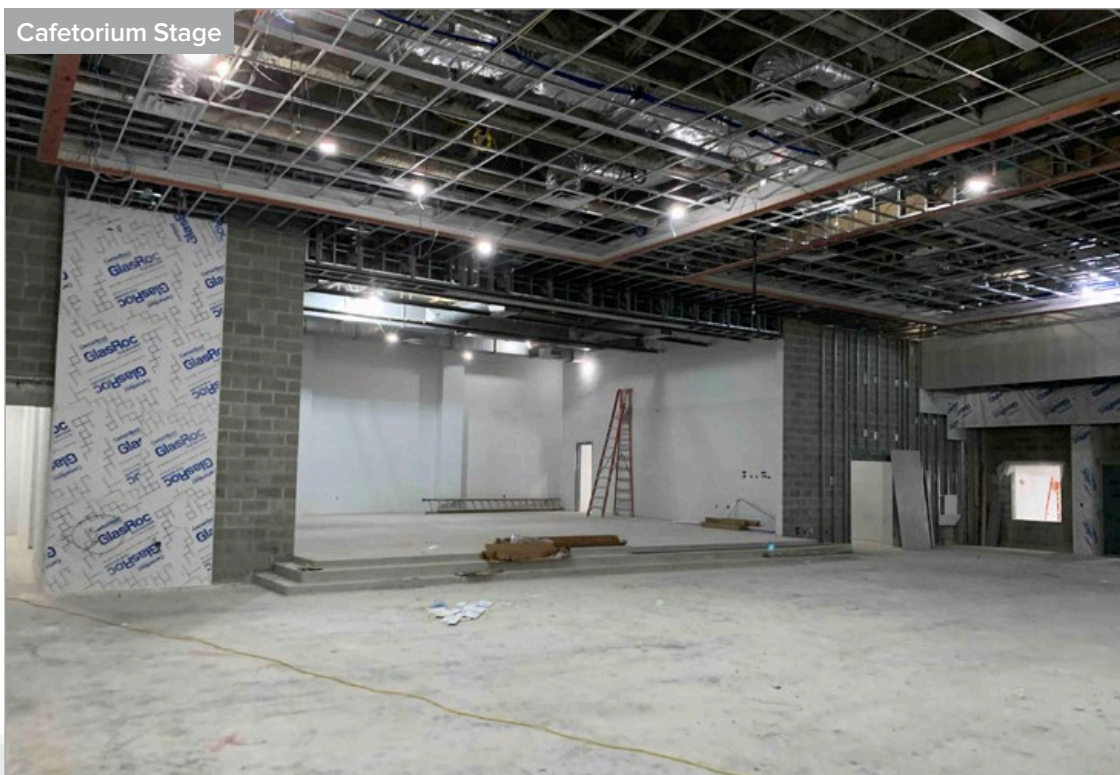

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF MARCH 2024

Kitchen



Competition Gymnasium



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF MARCH 2024

Locker Room



Rear Entry



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF MARCH 2024



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF MARCH 2024



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF MARCH 2024

WORK COMPLETED AND ONGOING:

- | Site | Building |
|---|---|
| <ul style="list-style-type: none">• Preparing to lime subgrade at access road to pump house• Drilling of irrigation water well complete• Liner and stone base installation ongoing at athletic field• Installation of site light poles ongoing• Installation of athletic light poles ongoing• One slab poured at tennis courts and another will be poured within two weeks• Masonry at concession stand to begin soon | <ul style="list-style-type: none">• Structural steel, joists, and metal deck erection ongoing in classroom area• The second-floor slab in area 10 will be poured next week.• Fireproofing of structural steel ongoing• Exterior studs and sheathing ongoing at classrooms• Interior metal studs, gypsum board, and MEP rough-in ongoing at classrooms• CMU masonry work ongoing – Areas 4 and 5• Roofing at competition gym ongoing |



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF MARCH 2024



LOOKING EAST
W. H. Moseley Middle School



LOOKING SOUTH
W. H. Moseley Middle School

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF MARCH 2024



LOOKING WEST
W. H. Moseley Middle School



Exterior Face Brick

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF MARCH 2024

Exterior Sheathing at Academic Wing



Steel Erection at Academic Wing



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF MARCH 2024

Student Commons



Academic Second Floor

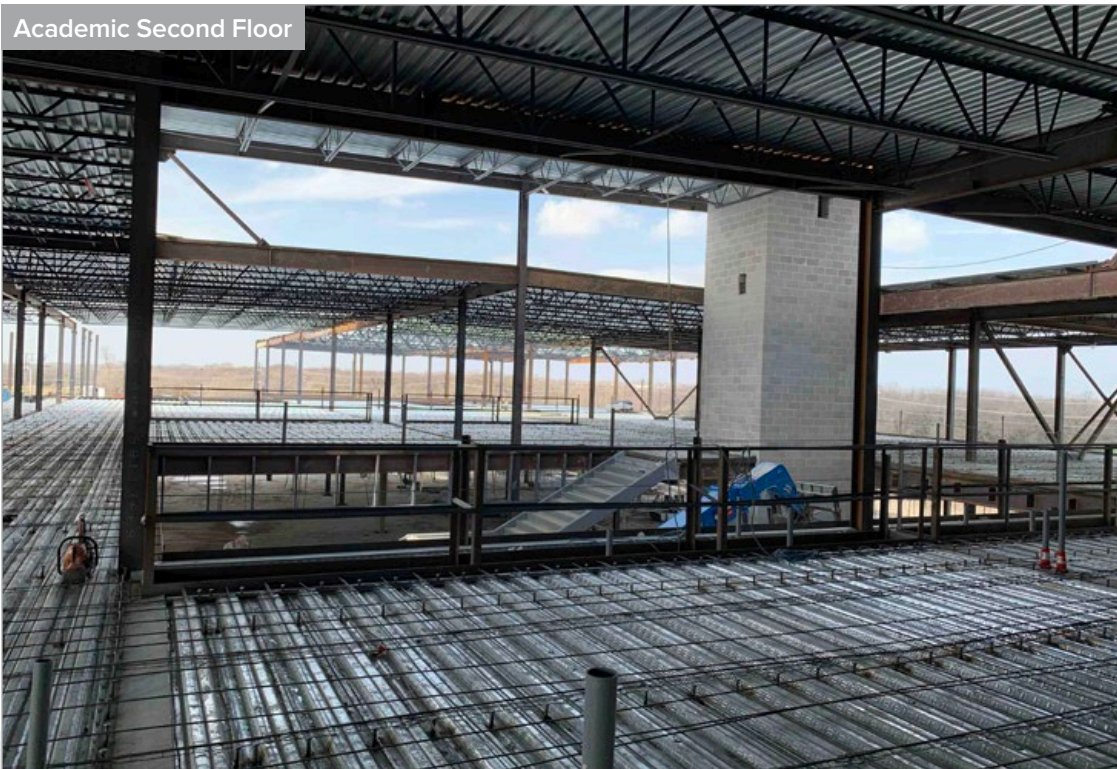

BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT




W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF MARCH 2024

Academic Corridor

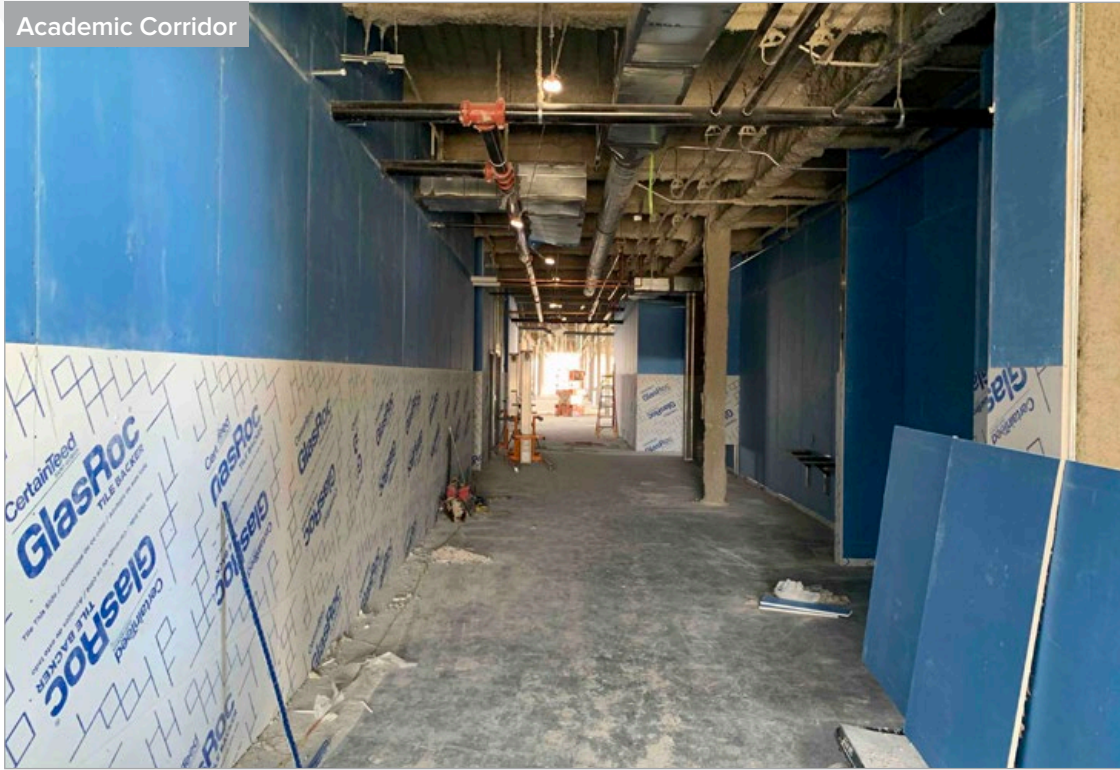

Competition Gymnasium

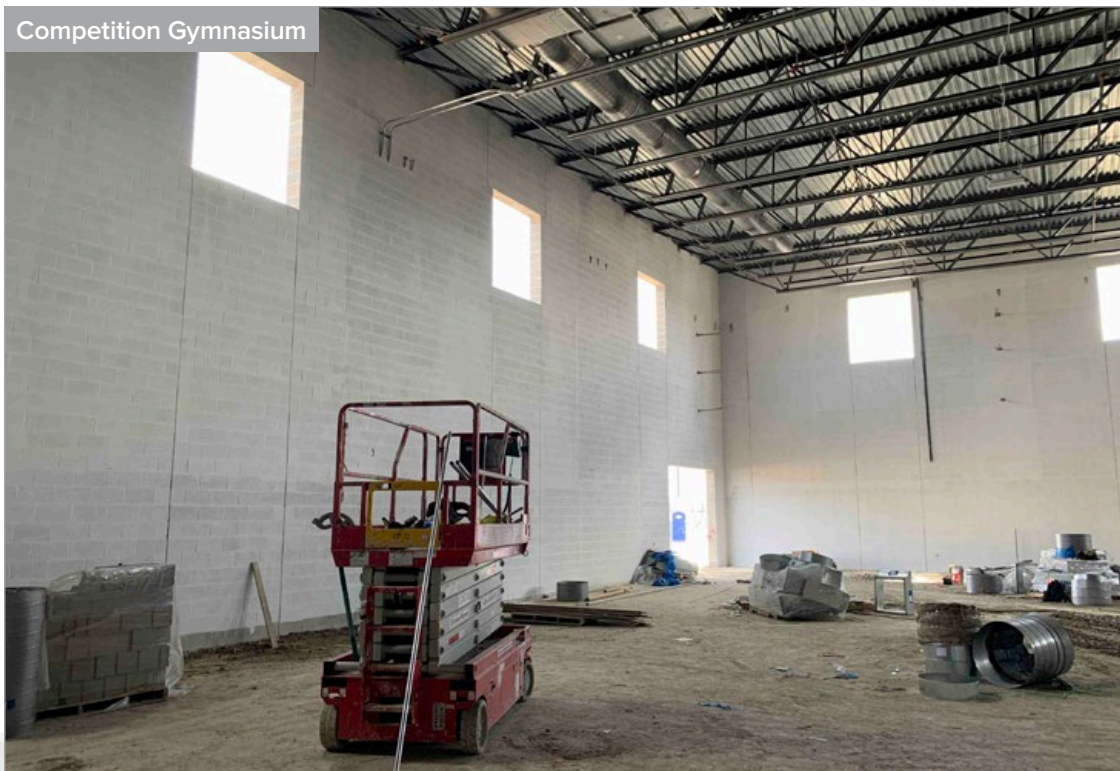

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF MARCH 2024

Secondary Gymnasium (Shelter)



Weight Room

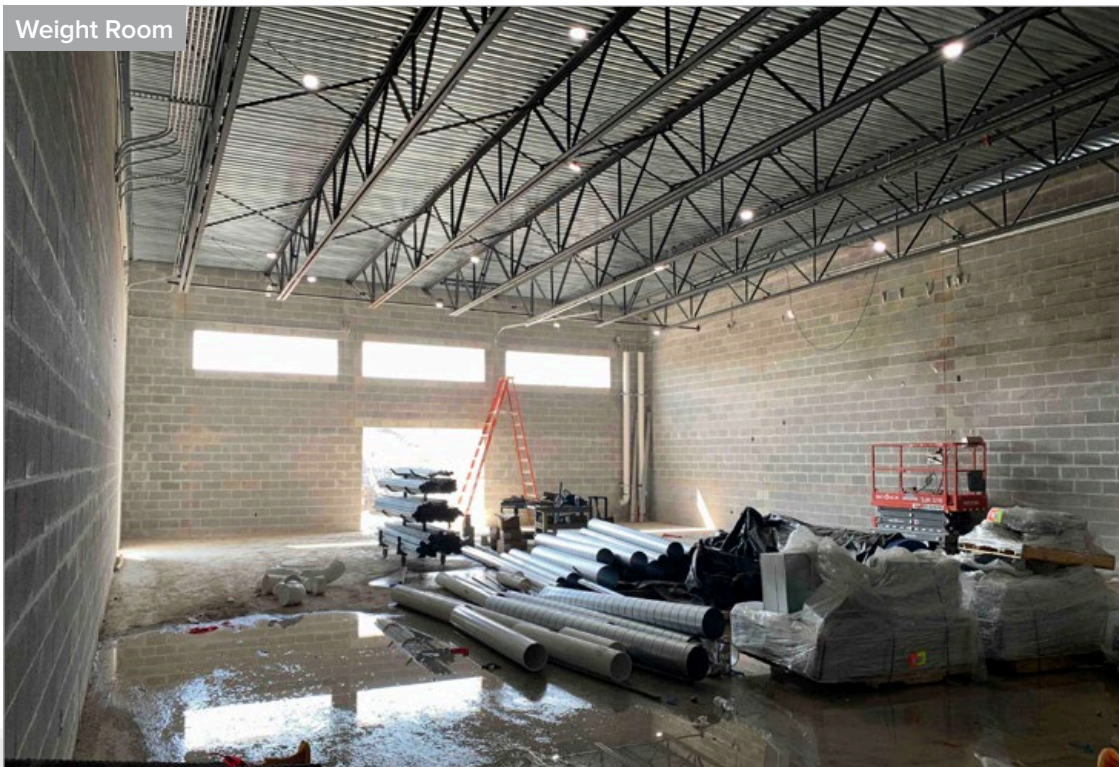

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF MARCH 2024

Kitchen/Fine Arts



Rear Entry

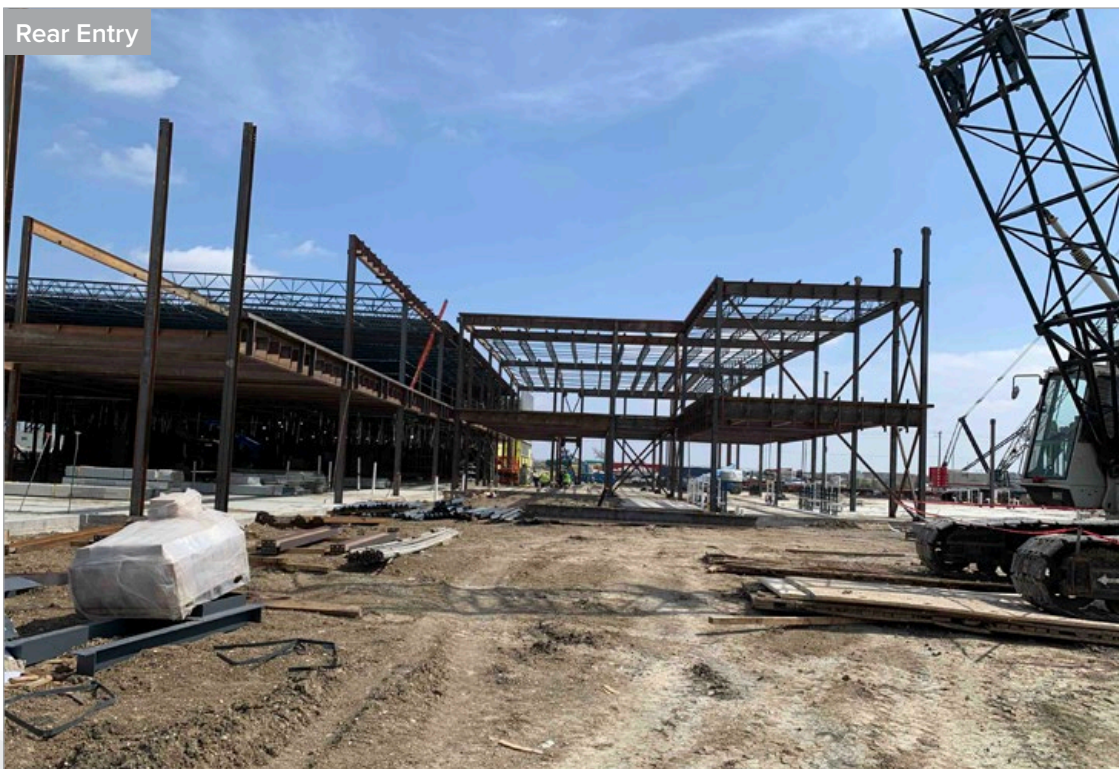

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF MARCH 2024

Concession Restroom Building



Track and Field



BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF MARCH 2024

Tennis Courts

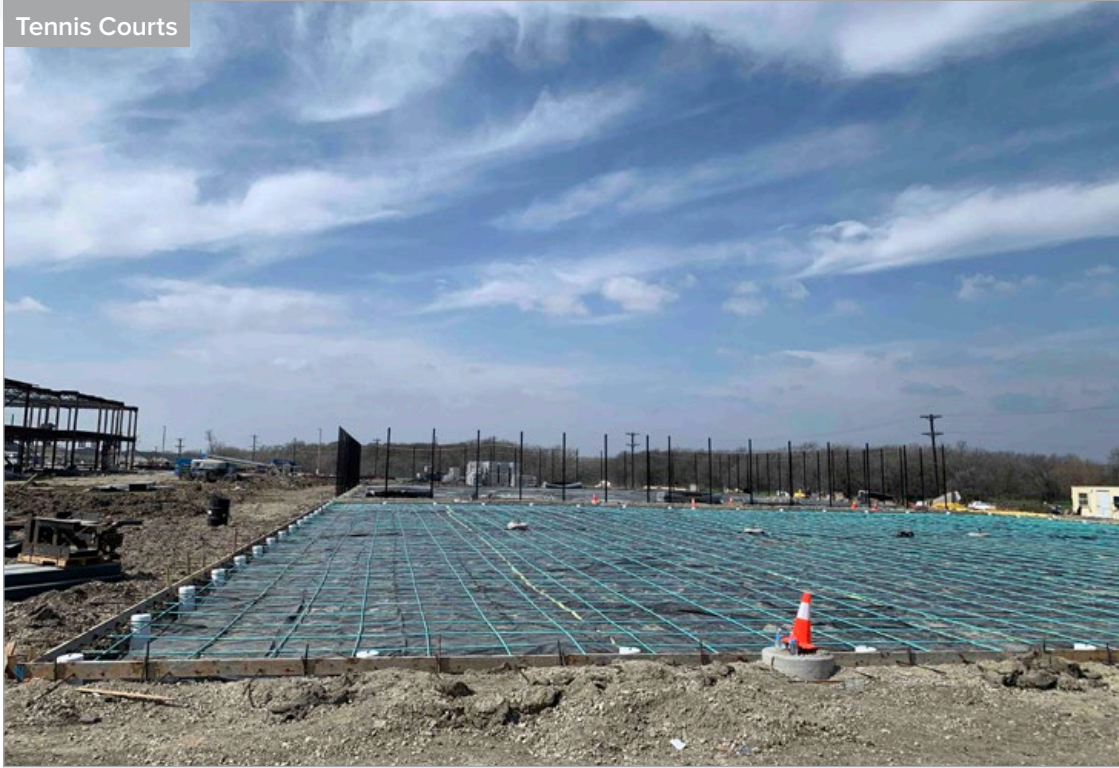

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF MARCH 2024

WORK COMPLETED AND ONGOING:

Site

- Moisture conditioning at all remaining fire lanes ongoing
- Utilities at Prairie Drive are complete; moisture conditioning ongoing
- Storm drain, water, sanitary sewer main runs, and majority of laterals complete; camera testing of water lines ongoing
- Plumbing at Multipurpose Facility (MPF) building complete
- MPF building grade beams complete
- Concrete placement for parking lots 3, 5 and 6 complete
- Tennis Court subgrade prep complete
- Moisture conditioning at baseball field ongoing
- Batting cages, dugouts, and irrigation well building grade beams ongoing

Building

- MEP underground complete – Areas A, B, C, P, Q, R and S; ongoing – Areas D and E
- Foundation pour complete – Area P
- Loadbearing CMU walls complete – Area R; ongoing – Area Q
- Structural steel ongoing – Areas A and B
- Concrete column installation ongoing – Areas D and N
- Slab on deck was pour complete – Area A




BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF MARCH 2024

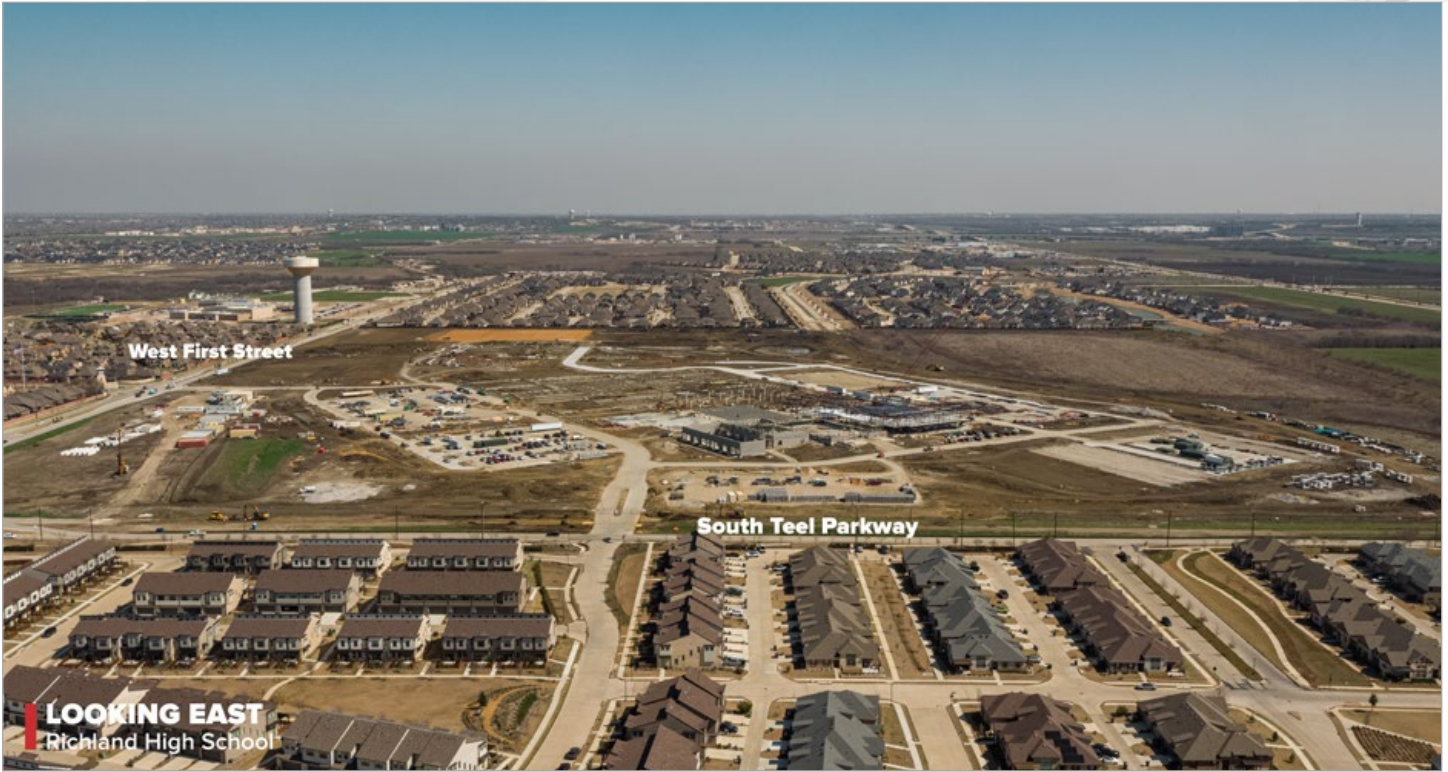


BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




RICHLAND HIGH SCHOOL (HS #4)

AS OF MARCH 2024

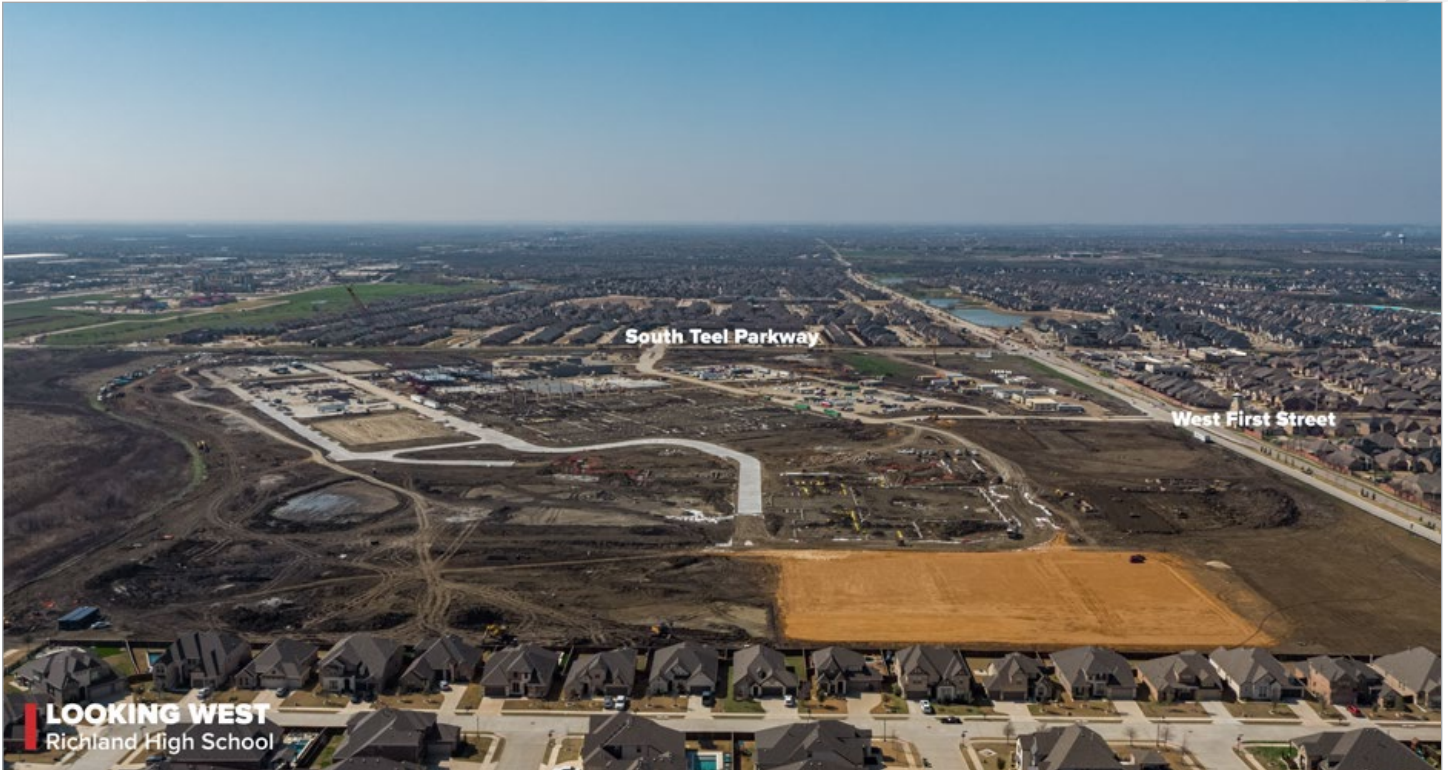

Main Entry Looking Down Colonnade of Student Union

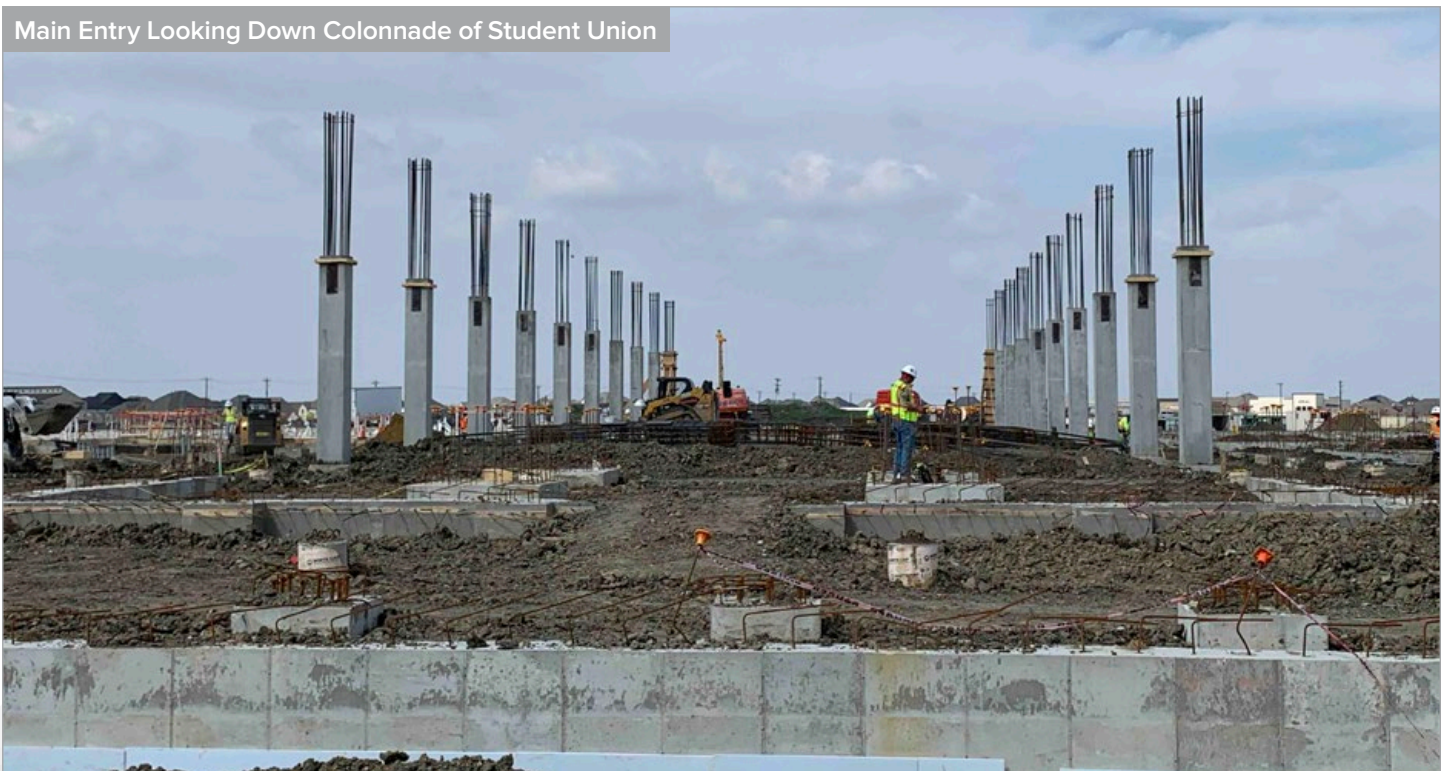

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF MARCH 2024

Main Street Corridor (West Academic Wing)



Main Street Corridor (West Academic Wing)



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




RICHLAND HIGH SCHOOL (HS #4)

AS OF MARCH 2024

Steel Erection



West Academic Courtyard

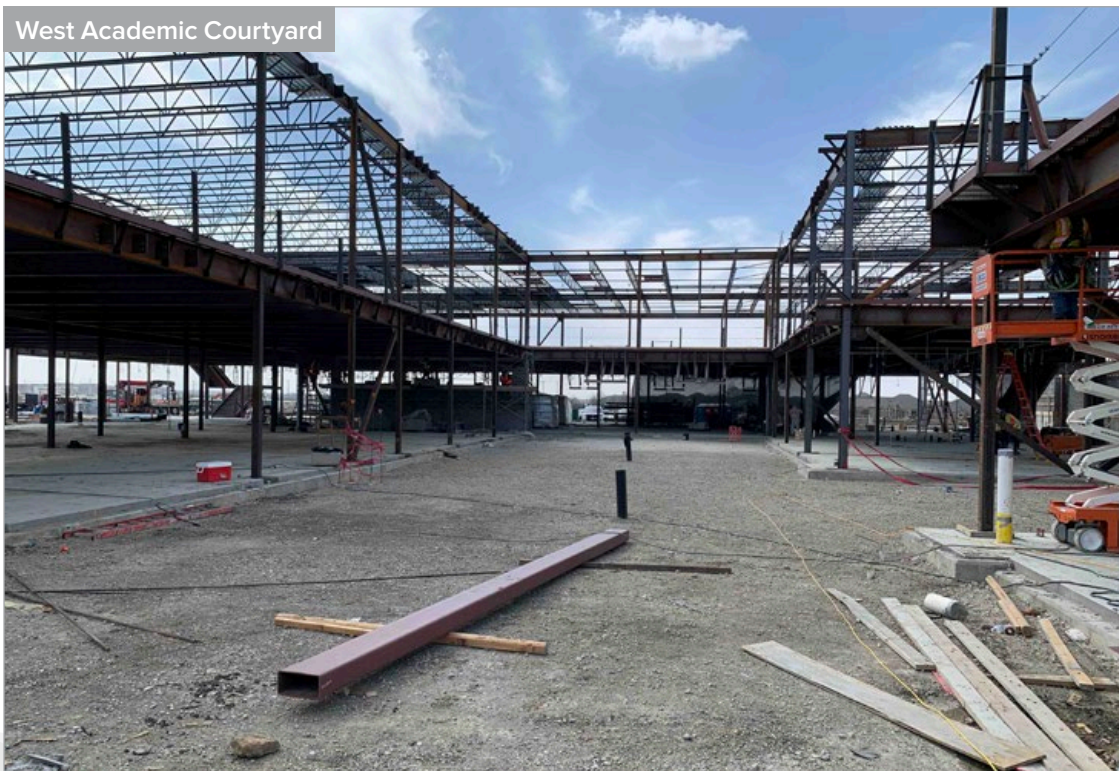

BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT




RICHLAND HIGH SCHOOL (HS #4)

AS OF MARCH 2024

West Academic Courtyard

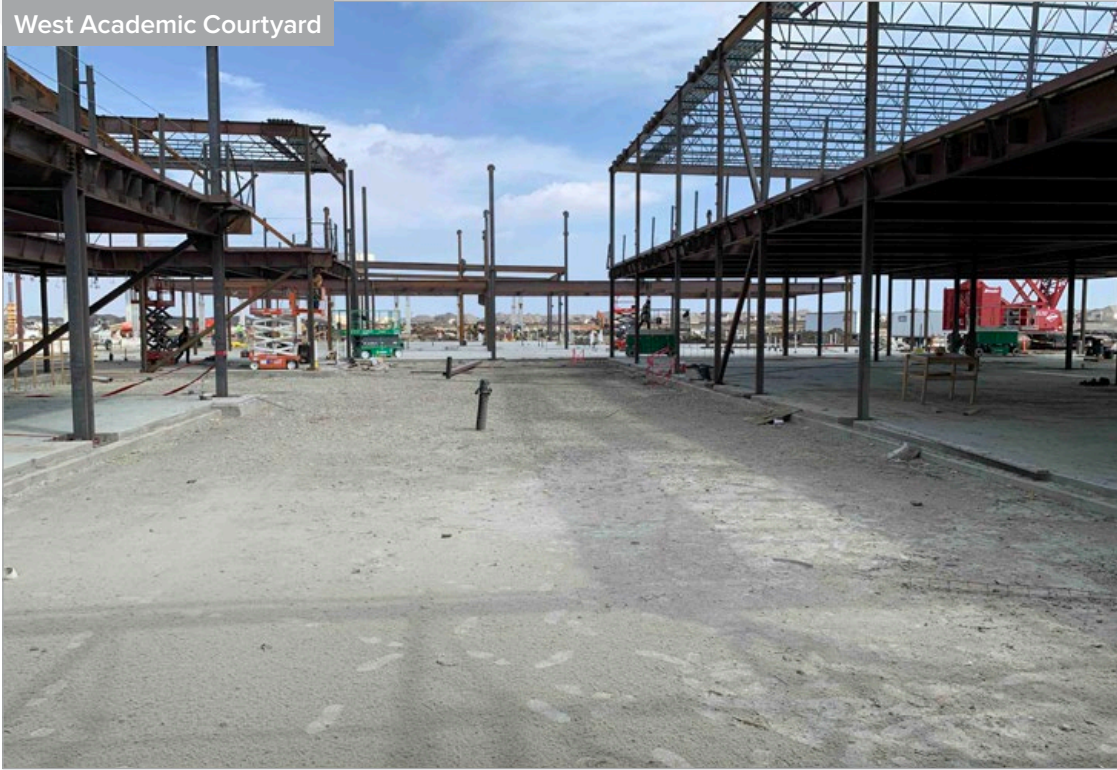

West Academic Wing Stairs

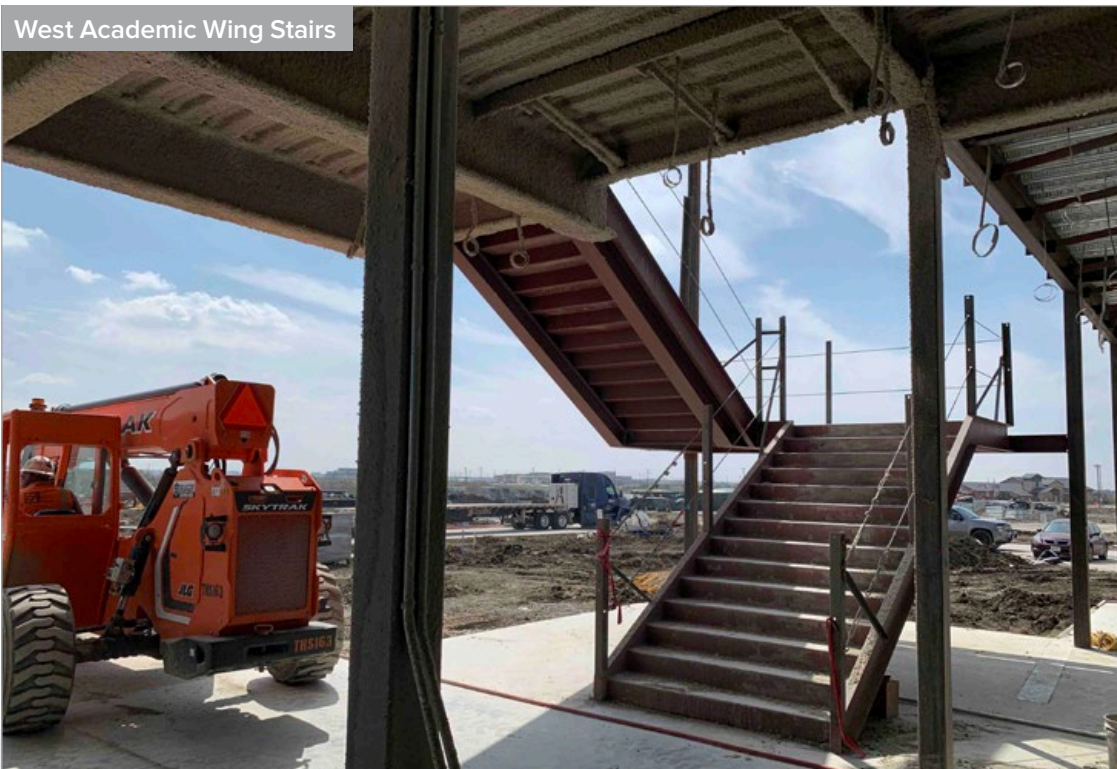

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




RICHLAND HIGH SCHOOL (HS #4)

AS OF MARCH 2024

Fireproofing



CMU Installation

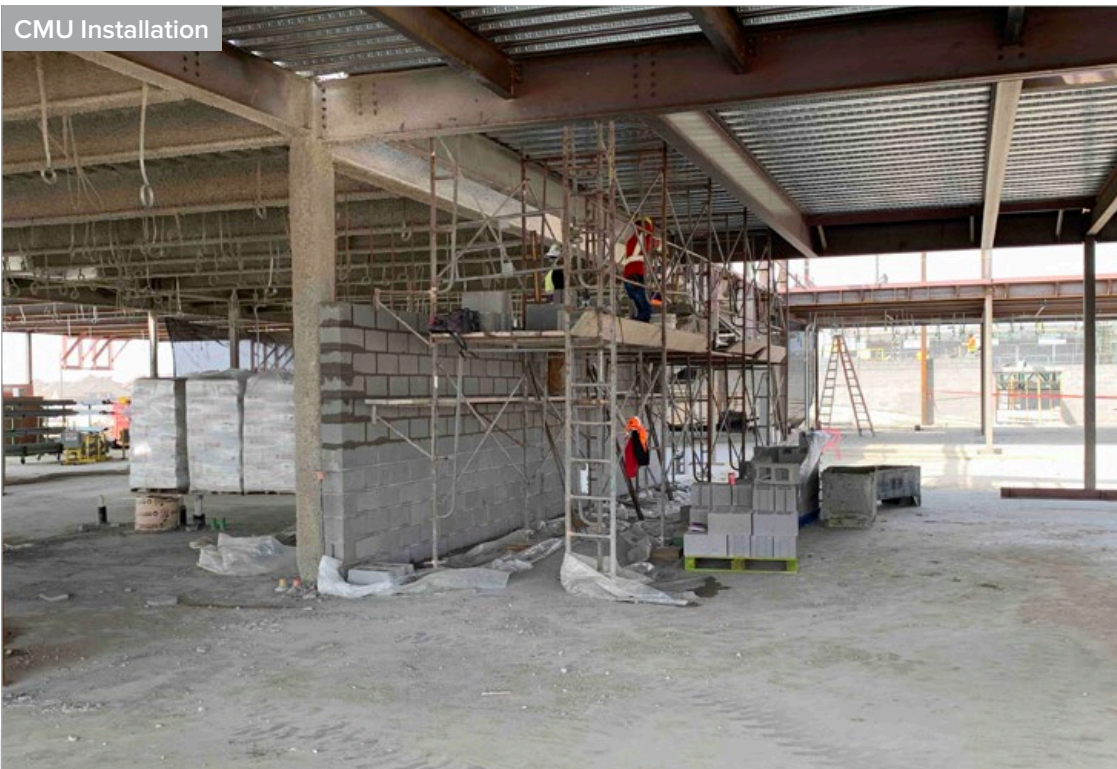

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF MARCH 2024

Fine Arts



Art Classrooms (Interior)



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF MARCH 2024

Art Classrooms (Exterior)



Multi-Purpose Facility Grade Beams



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF MARCH 2024

Multi-Purpose Facility Grade Beams



Multi-Purpose Facility Structural Steel

