

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF SEPTEMBER 2023

WORK COMPLETED AND ONGOING:

Site

- Pier drilling ongoing
- Utilities ongoing throughout the site

Building

- Grade beam installation ongoing



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF SEPTEMBER 2023



LOOKING EAST

Betty Jackson Elementary School



LOOKING SOUTH

Betty Jackson Elementary School

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF SEPTEMBER 2023



LOOKING WEST

Betty Jackson Elementary School

Site Utility Installation



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF SEPTEMBER 2023

Pier Installation



Excavation for Grade Beam Formwork



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF SEPTEMBER 2023

Grade Beam Formwork



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF SEPTEMBER 2023


WORK COMPLETED AND ONGOING:

Site

- Added Coit Road turn lanes complete
- Football field subgrade prep ongoing
- Flatwork grading along Prestwick ongoing
- Pump house slab pour complete
- CMU installation at pump house ongoing
- All paving complete
- Flume installation in west detention pond ongoing
- Light pole installation 95% complete
- Concession stand CMU installation ongoing

Building

- Exterior framing ongoing – Areas 1, 2 and 3
- Fireproofing ongoing – Areas 1, 2 and 3
- MEP rough-in ongoing – Areas 1, 2, 3, 5, 6 and 7
- MEP overhead ongoing – Areas 2 and 3
- CMU installation ongoing – Areas 4, 5 and 6
- Steel roof framing ongoing – Areas 5, 6 and 9
- Steel roof framing complete – Areas 7, 10 and 11
- All 2nd floor slab pours complete
- Exterior air barrier installation ongoing
- Exterior veneer installation ongoing
- Slab pour complete – Area 8

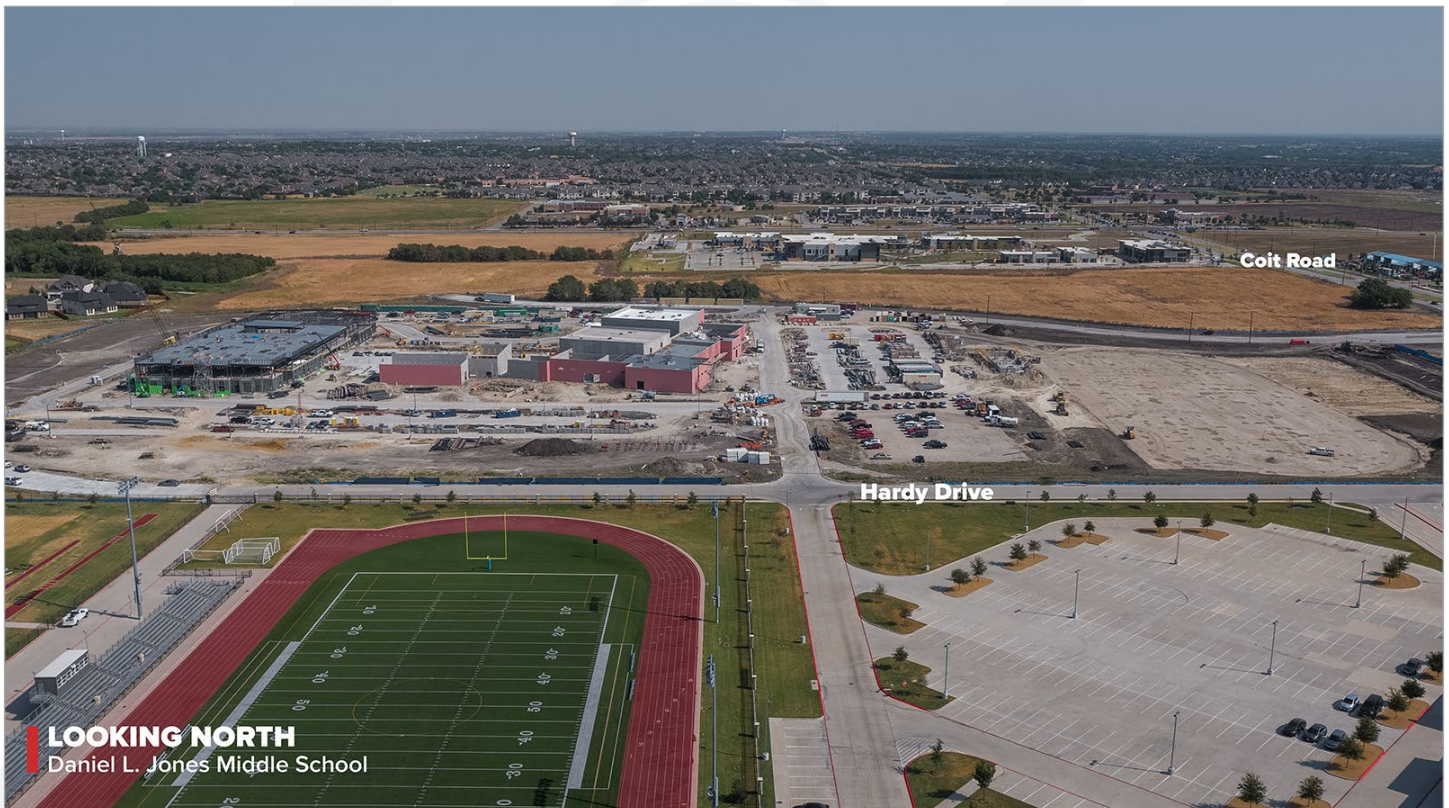

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF SEPTEMBER 2023



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF SEPTEMBER 2023



LOOKING WEST
Daniel L. Jones Middle School

Exterior Masonry Progress



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF SEPTEMBER 2023


Academic Wing Progress



Academic Wing - Exterior Wall Sheathing Installation



Academic Wing Corridor

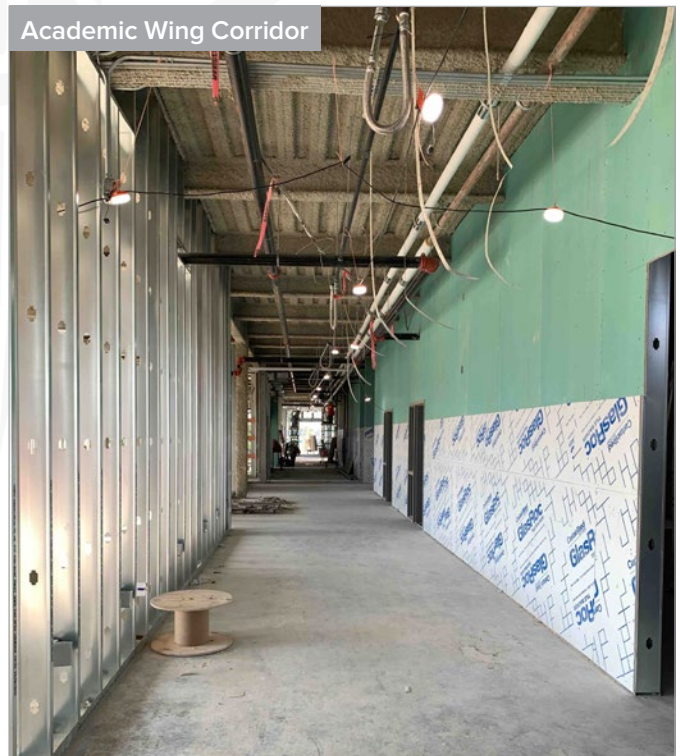

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF SEPTEMBER 2023

Academic Wing



HVAC Ductwork



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF SEPTEMBER 2023

Competition Gymnasium



Ancillary Gymnasium (Shelter)



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF SEPTEMBER 2023

WORK COMPLETED AND ONGOING:

Site

- Grading of site and building pad ongoing
- Test piles results received, updating documents in accordance with test pile results/recommendations
- Town prefers to issue building permit once final civil/structural drawings are complete, incorporating test pile results and flood study updates
- Civil Engineer and Town are working diligently on getting flood study approved
- Production piles and underground MEP utilities will begin once updated documents are received and approved by the Town, and building permit is issued
- All parties involved have made building permit the main focus



LOOKING NORTH
W. H. Moseley Middle School


BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF SEPTEMBER 2023

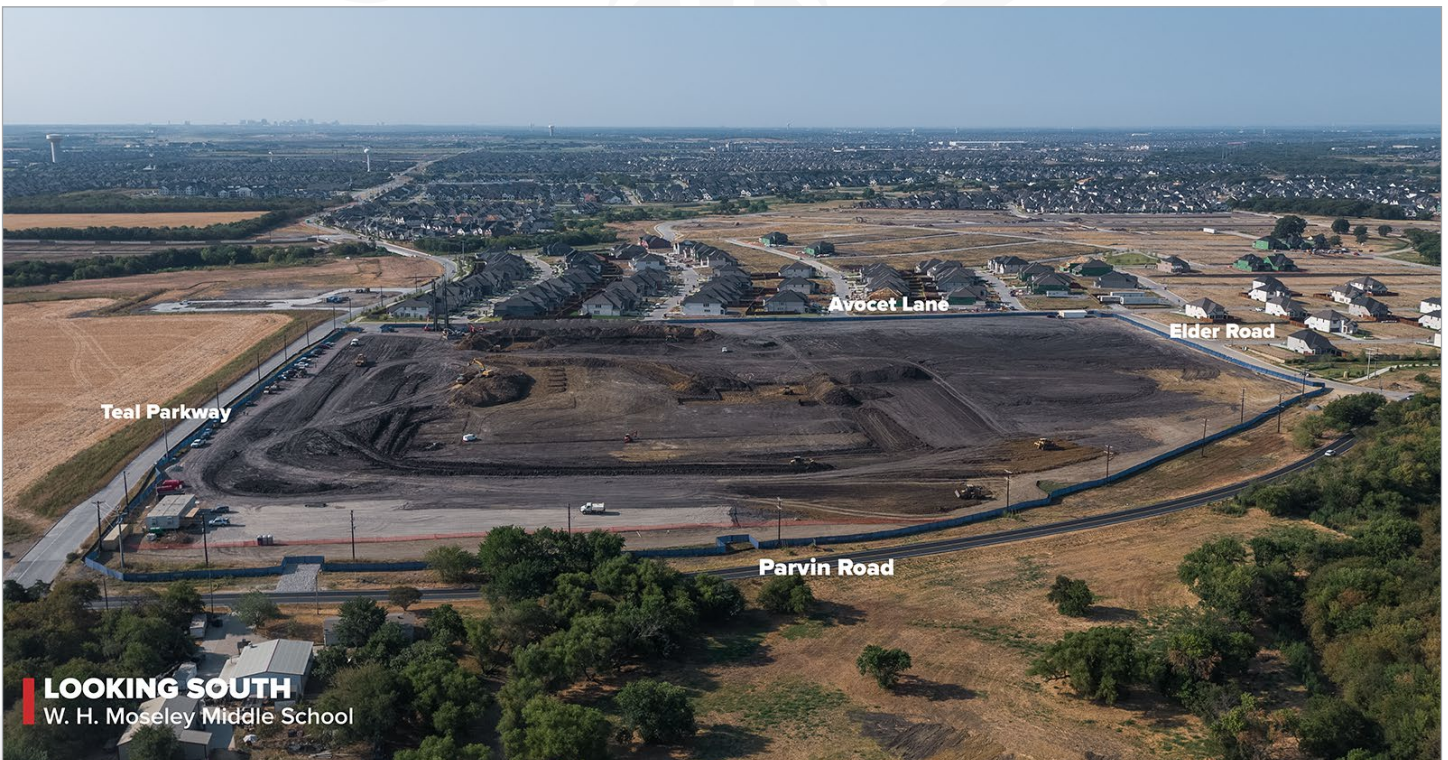

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF SEPTEMBER 2023



LOOKING WEST
W. H. Moseley Middle School

Earthwork



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF SEPTEMBER 2023

Earthwork



Earthwork



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF SEPTEMBER 2023

Pier Drilling Rigs Onsite



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF SEPTEMBER 2023

WORK COMPLETED AND ONGOING:

Site

- Site grading is ongoing
- Utility installation is ongoing (on-site only)
- Off-site Civil release still pending due to Atmos gas line

Building

- Test piles are complete
- Geotech design recommendations are currently being reviewed by structural
- Building piles to begin immediately after updated pile design is released



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF SEPTEMBER 2023



LOOKING EAST
Richland High School



LOOKING SOUTH
Richland High School

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF SEPTEMBER 2023



Earthwork



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF SEPTEMBER 2023

Earthwork



Earthwork



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF SEPTEMBER 2023

Earthwork

