

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF JANUARY 2024

WORK COMPLETED AND ONGOING:

Site

- Site paving complete
- Irrigation 65% complete
- Site lighting powered up mid-January
- City sidewalk 95% complete

Building

- Roofing ongoing
- Masonry ongoing
- Permanent power installed
- Clerestory ongoing
- Wall framing ongoing
- CMU block complete – Area 4
- Kitchen equipment delivery and installation upcoming
- Pouring cafetorium stage
- Ceramic wall tile in kitchen and cafeteria to start mid-January



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF JANUARY 2024



LOOKING EAST

Betty Jackson Elementary School



LOOKING SOUTH

Betty Jackson Elementary School

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF JANUARY 2024



Main Entry



BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT




BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF JANUARY 2024

Main Entry Corridor

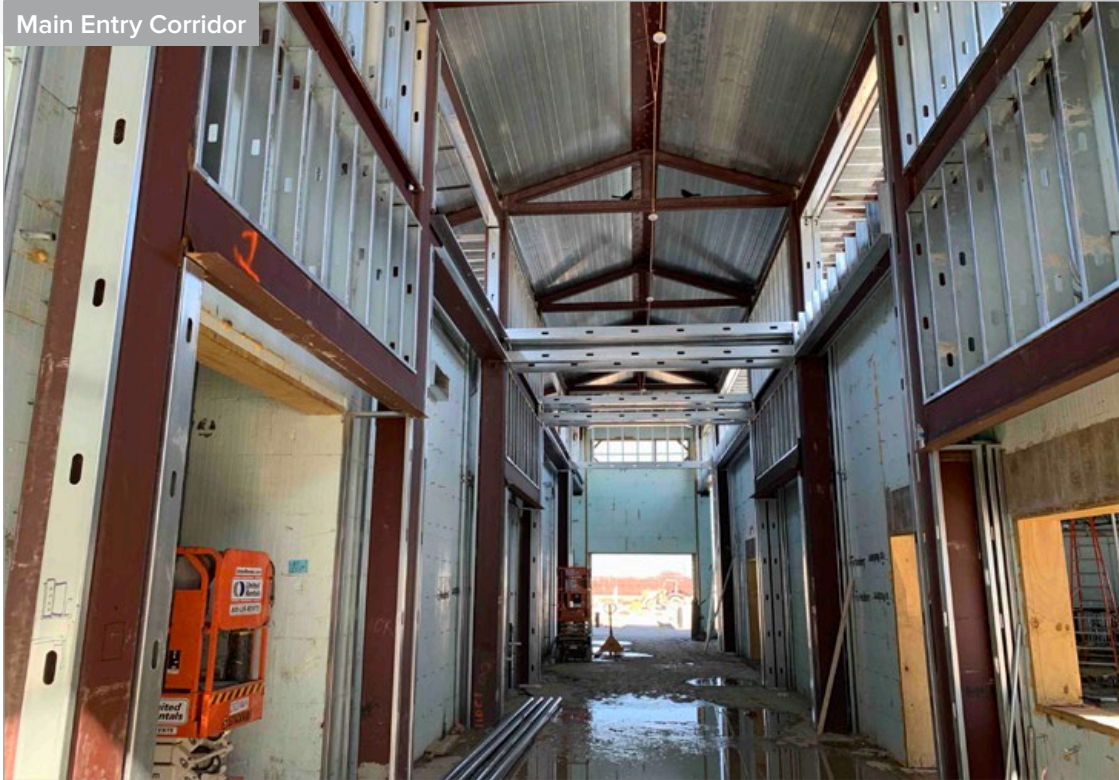

Academic Corridor

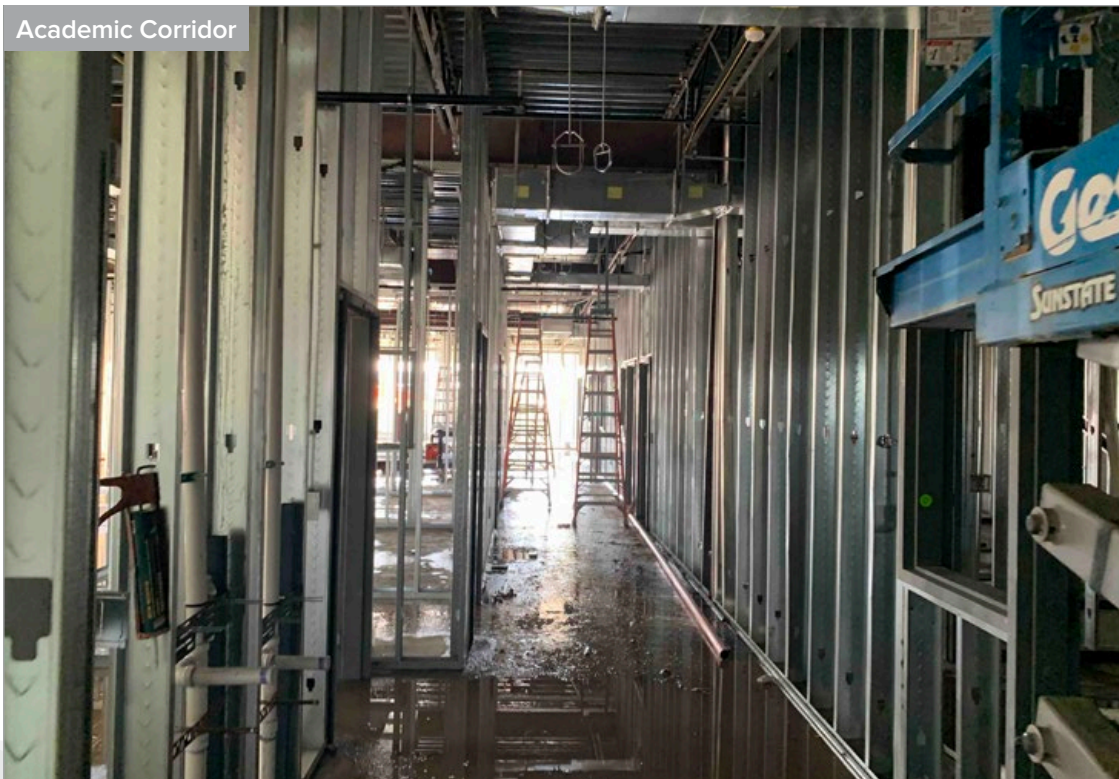

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF JANUARY 2024

Multi-user Restroom Plumbing



Steel Joist Erection




BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF JANUARY 2024

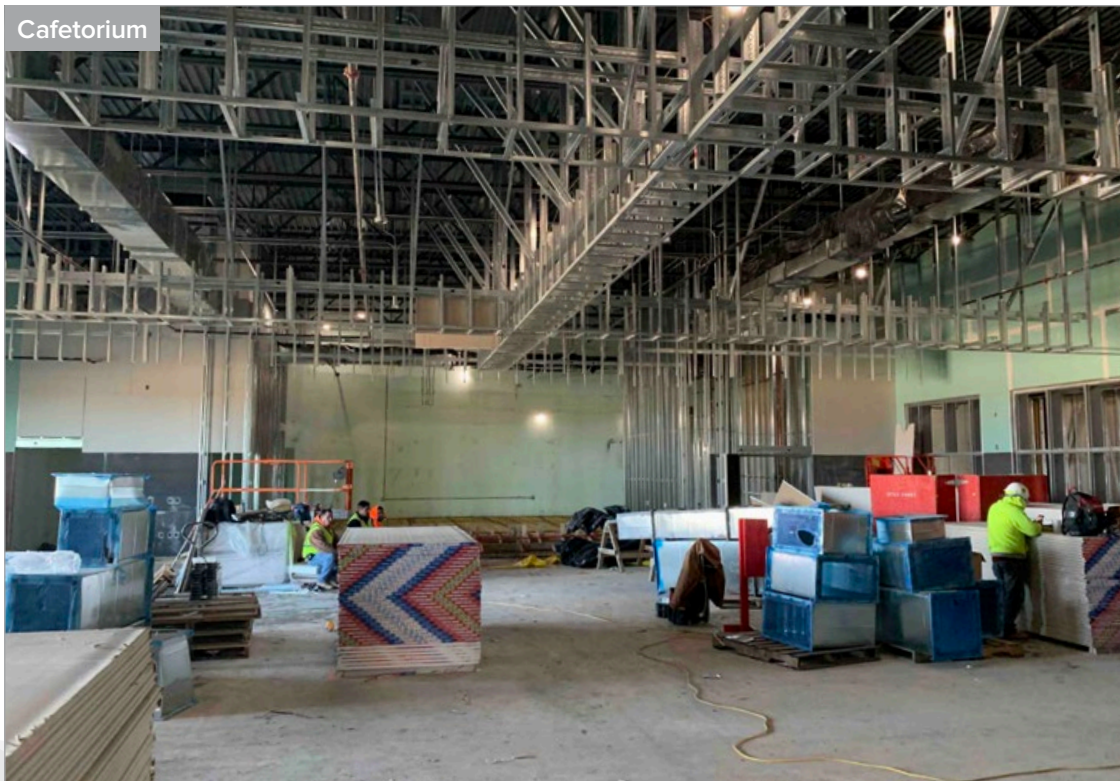


BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF JANUARY 2024

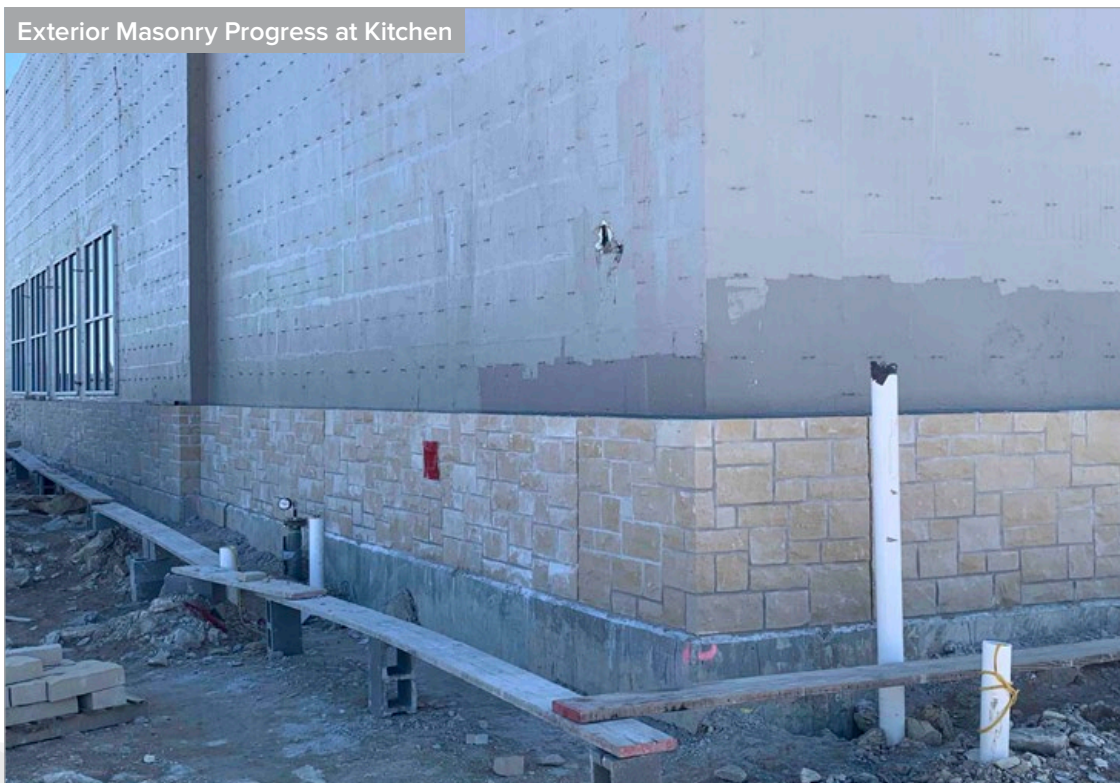

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

AS OF JANUARY 2024

Rear Entry



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF JANUARY 2024

WORK COMPLETED AND ONGOING:

Site

- Football field subgrade preparation ongoing; trench drain installation complete
- Sports lighting at football field and tennis courts complete
- Tennis court concrete complete; fence ongoing
- Sidewalk installation along Prestwick complete
- Masonry veneer at pump house complete
- Flume installation in west detention pond complete
- Light pole installation complete
- Concession building masonry veneer complete
- Final grading and topsoil installation ongoing
- Scoreboard and time clock installation complete
- Football field and tennis court flatwork ongoing

Building

- Exterior sheathing complete
- Storefront window installation is 90% complete – Areas 1, 2, 3, 9, 10 and 11

- MEP rough-in ongoing
- Interior wall framing ongoing – Areas 4, 8 and 11
- Two-siding sheetrock – Areas 9, 10 and 11
- Tape, bed, and paint ongoing – Areas 1, 2, 3, 5, 6 and 7
- Tile installation ongoing in multi-user restrooms and academic corridors
- Building steel erection complete
- Concrete masonry unit (CMU) 99% complete; patching ongoing
- Locker base installation complete
- Tornado Shelter MEP rough-in ongoing
- Air barrier installation complete – Area 4
- Exterior veneer ongoing – Areas 1, 2, 3, 4, 5, 8, 9, 10 and 11
- Exterior veneer complete – Areas 6 and 7
- Roofing complete – Areas 5, 6, 7, 9, 10 and 11
- Roofing 90% complete – Areas 4 and 8
- Roof Top Unit (RTU) installation complete



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF JANUARY 2024



LOOKING EAST
Daniel L. Jones Middle School



LOOKING SOUTH
Daniel L. Jones Middle School

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF JANUARY 2024



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF JANUARY 2024

Main Building Entry



Main Entry




BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF JANUARY 2024

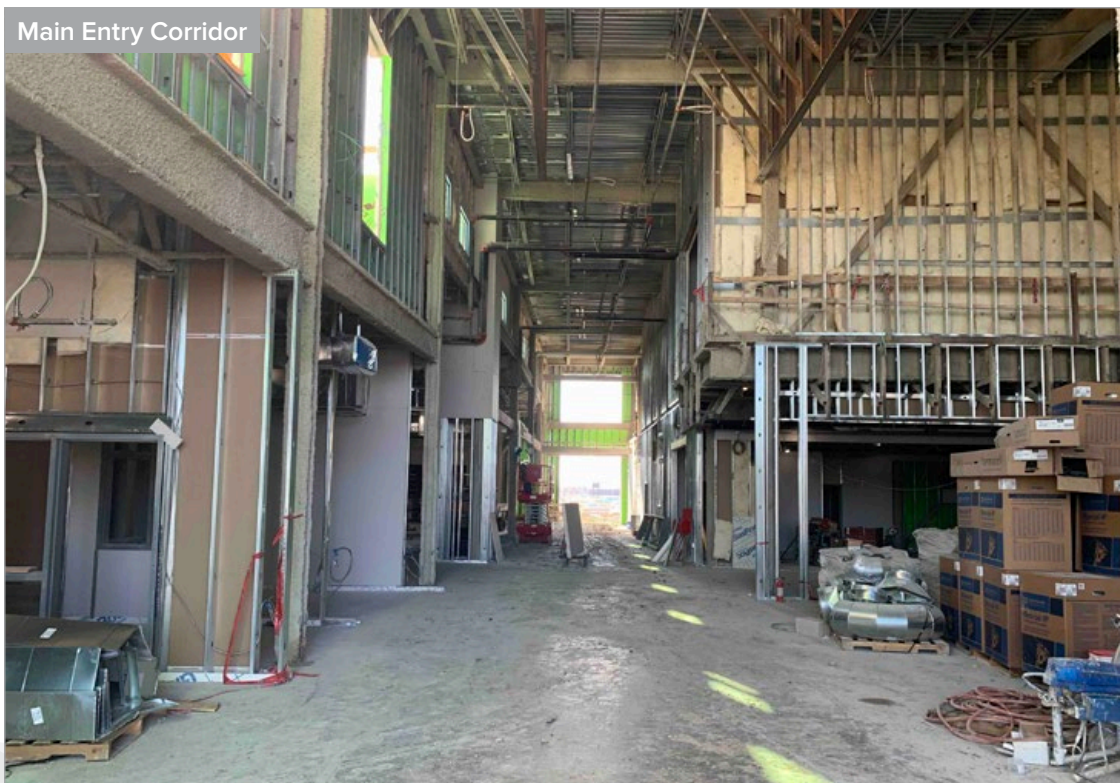

BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF JANUARY 2024

Library

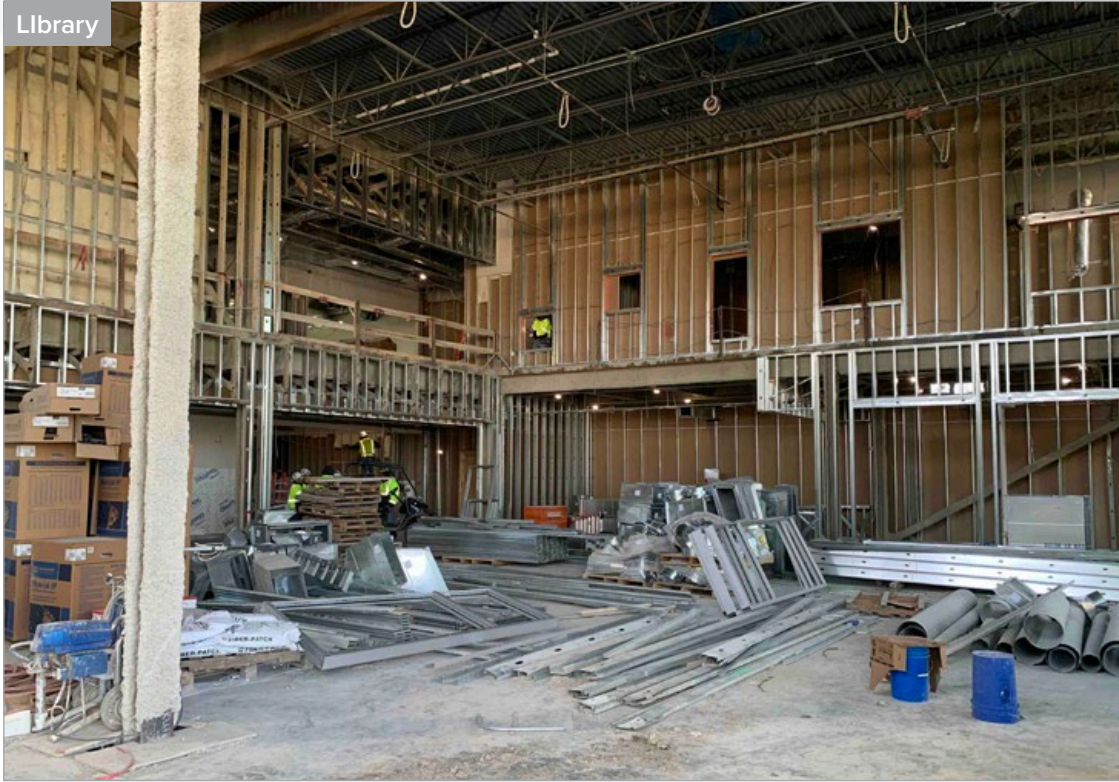

Computer Lab

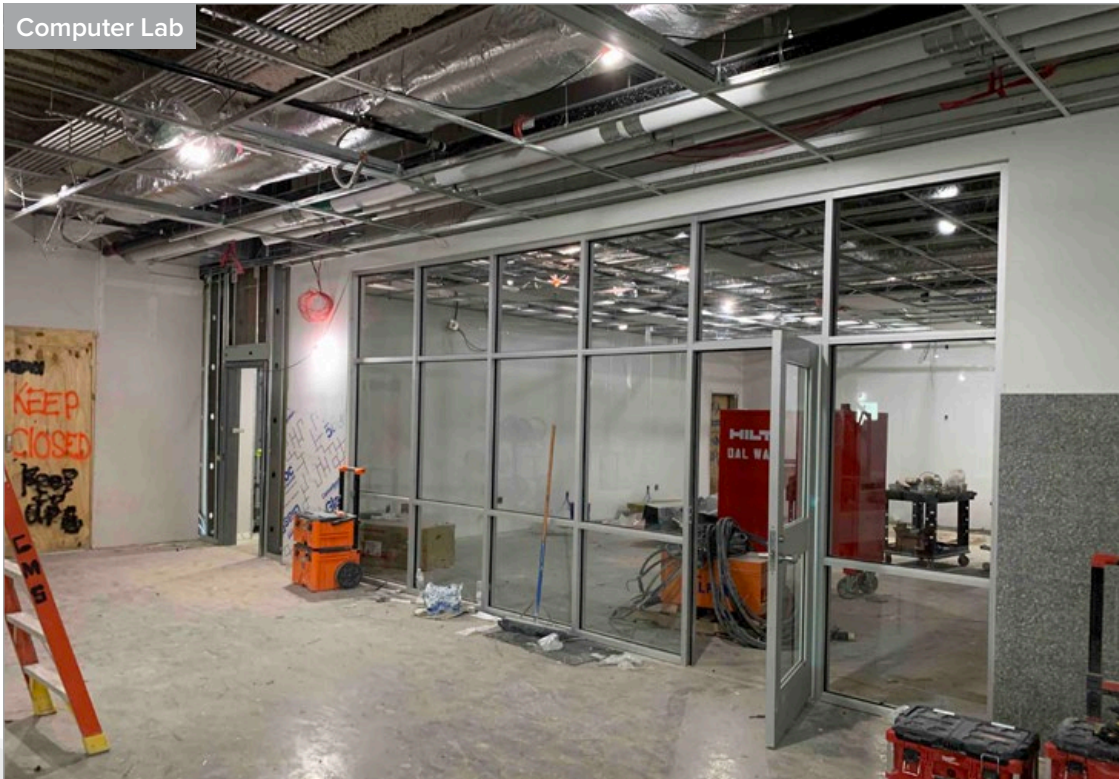

BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF JANUARY 2024

Academic Corridor

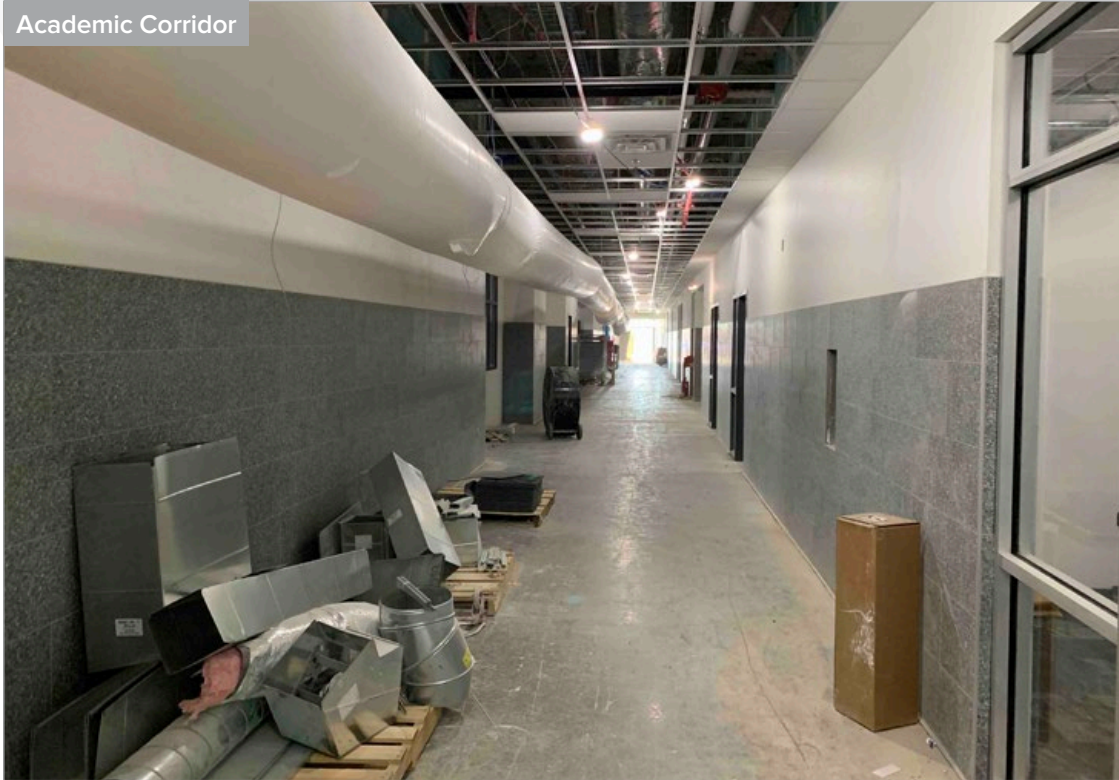

Student Commons

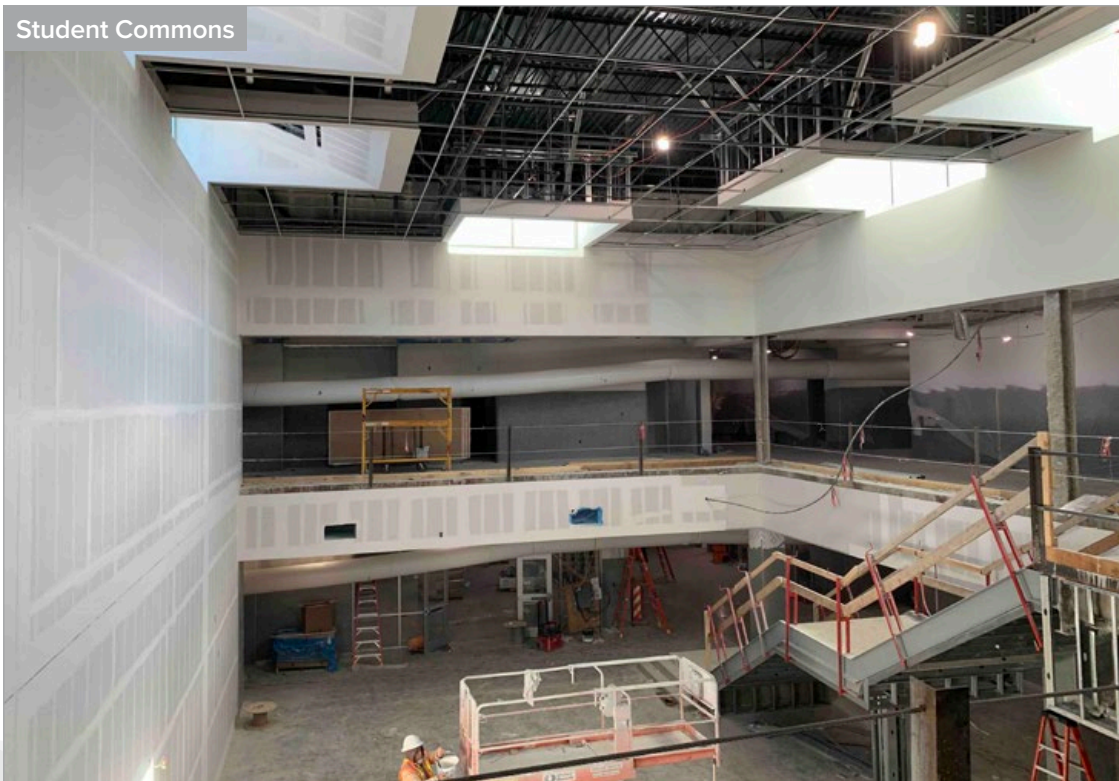

BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF JANUARY 2024

Multi-user Restroom Tile

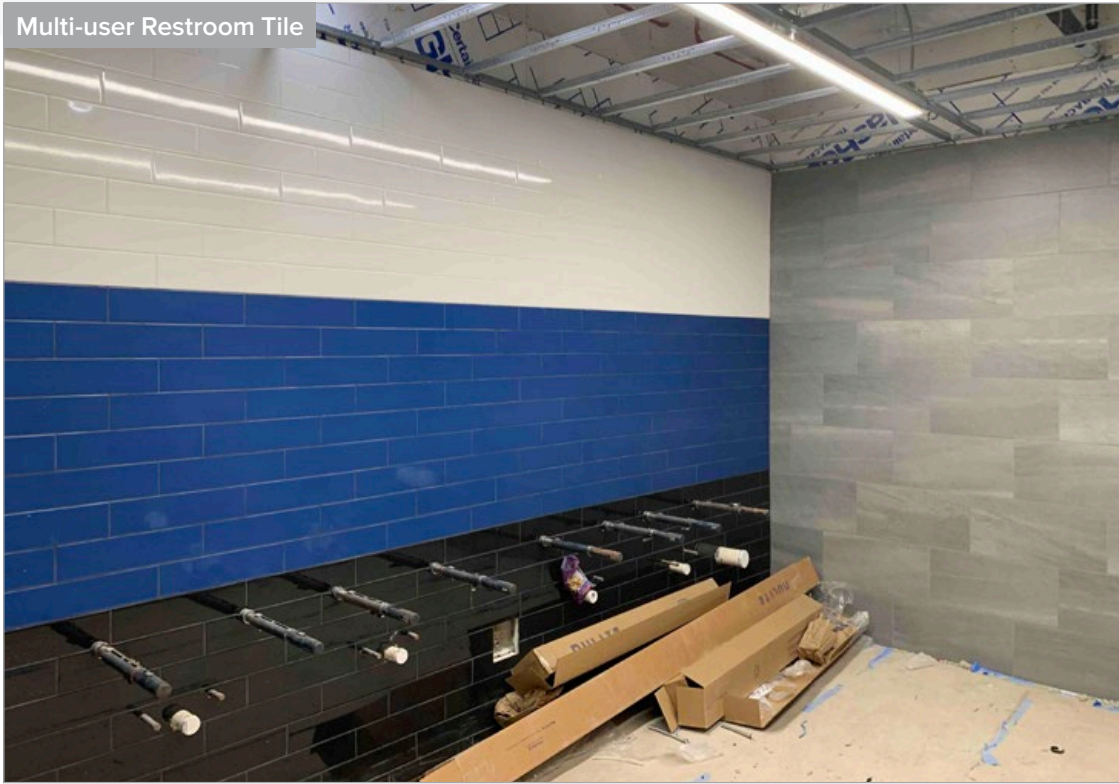

Cafetorium



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF JANUARY 2024

Collaboration Area



Secondary Gymnasium (Shelter)

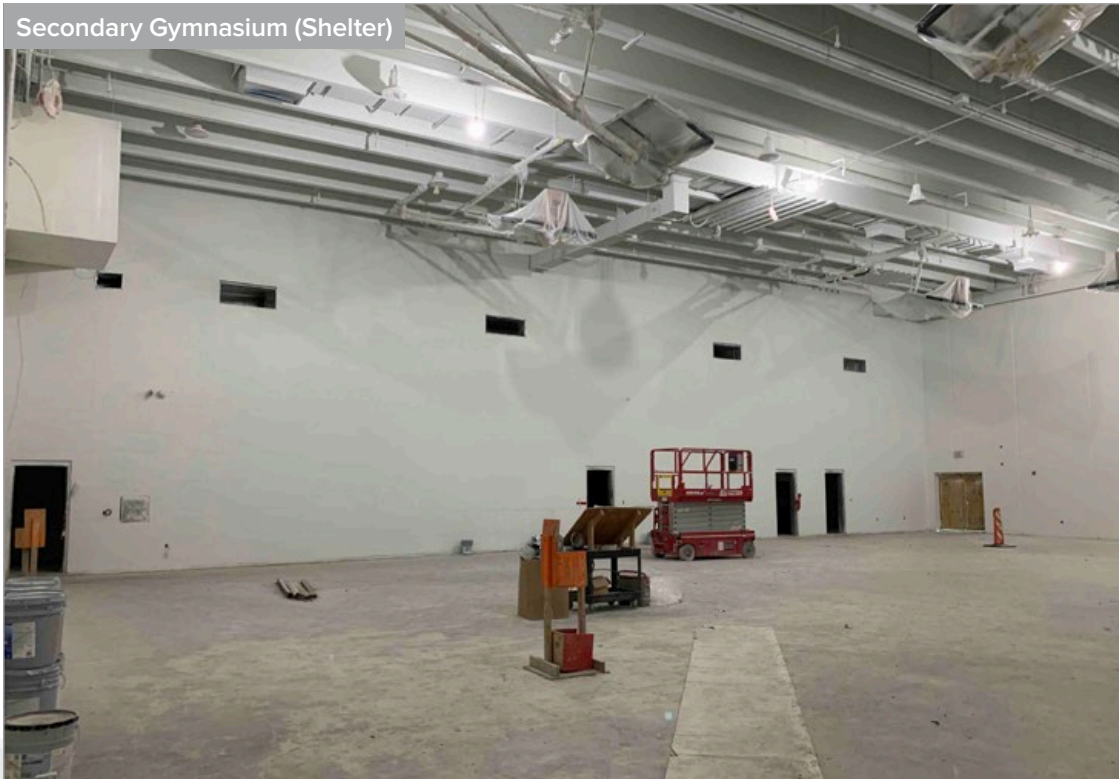

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF JANUARY 2024

Competition Gymnasium



Locker Room



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF JANUARY 2024

Exterior Masonry - Athletic Wing



Rear Entry




BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF JANUARY 2024

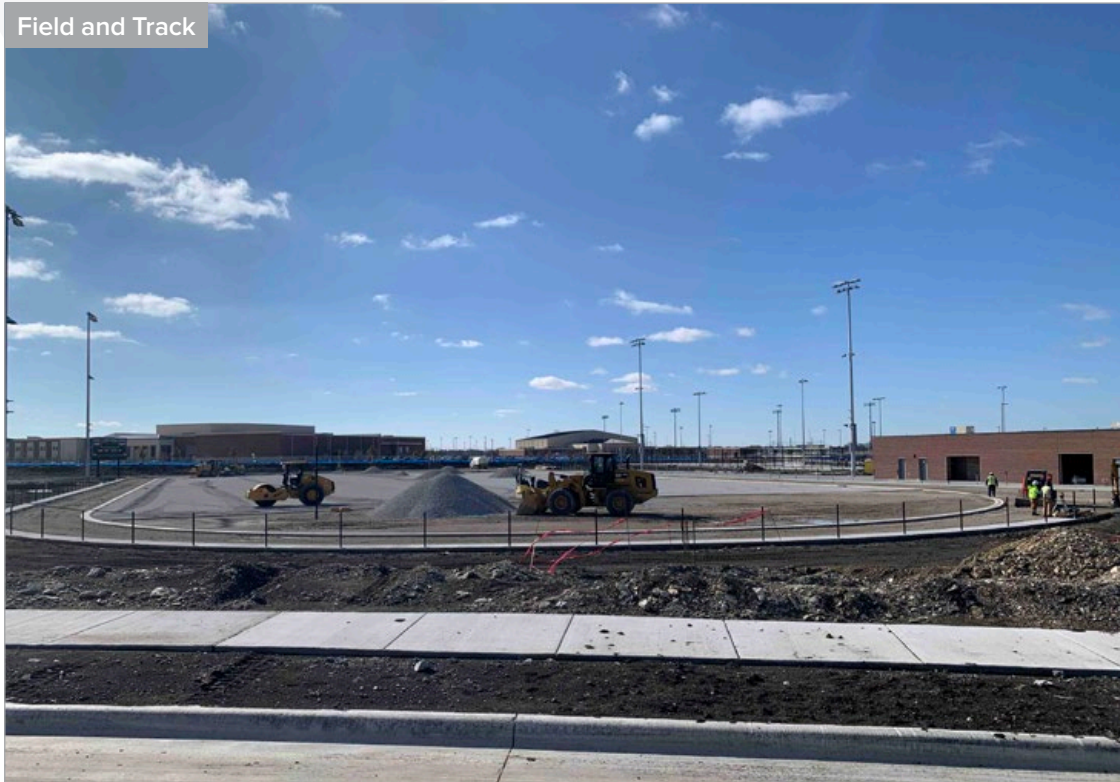

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF JANUARY 2024

WORK COMPLETED AND ONGOING:

Site

- Concrete paving at parking lots complete
- Paving for fire lanes on east side of building complete; one remaining concrete pour for fire lane on west side of building
- Drilling of irrigation water well will be complete this month
- Drainage installation at athletic field ongoing; to be followed by concrete curbs and asphalt at track
- Remaining site utility work on west side of site will be complete this month
- Concrete work associated with light pole bases ongoing
- Concrete work for tennis courts will start within next two weeks
- Building slab at concession building will be poured within next two weeks

Building

- Building slabs complete with the exception of the storm shelter and area left out for access to storm shelter through west side of Area 5
- Structural steel erection ongoing – Area 1
- Erection of precast panels and tees at the storm shelter will start this month
- Plumbing rough-in at restrooms ongoing in multiple areas.
- Concrete masonry unit (CMU) block work ongoing – Area 7
- Cold formed metal framing will start this month – Area 1



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF JANUARY 2024



LOOKING EAST
W. H. Moseley Middle School



LOOKING SOUTH
W. H. Moseley Middle School

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF JANUARY 2024



Concrete Drive Placement



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF JANUARY 2024

Concrete Masonry Unit (CMU) Block Progress - Athletics



Athletic Corridor

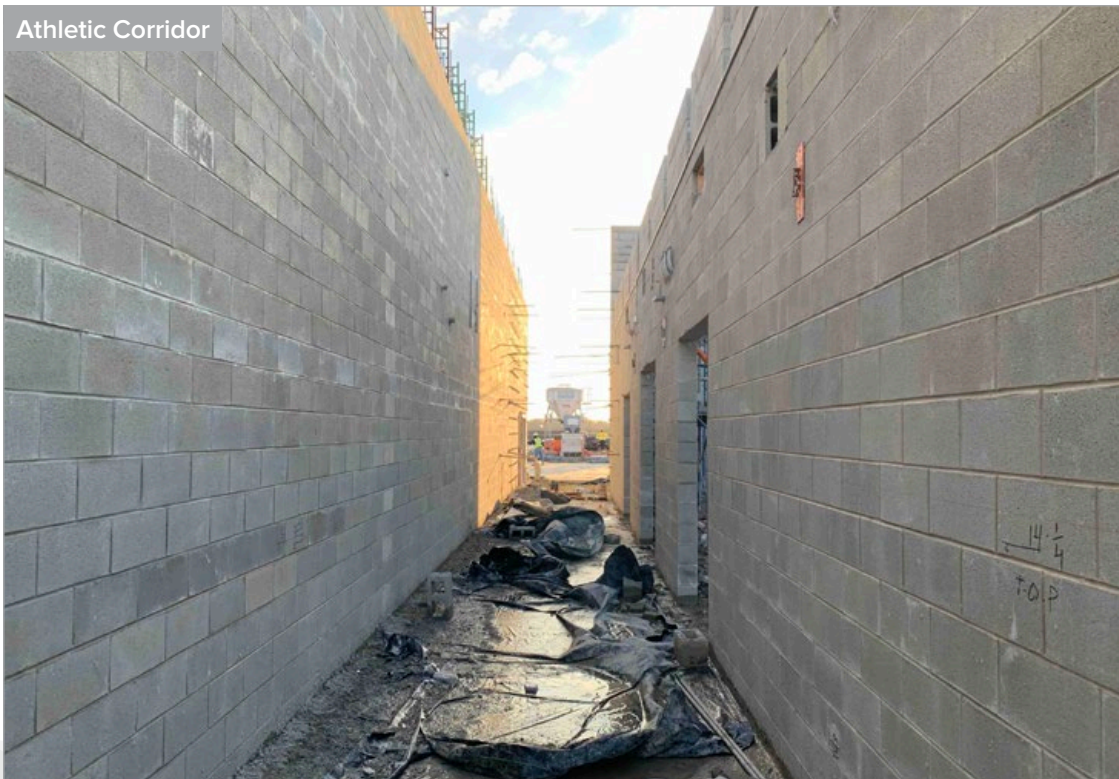

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF JANUARY 2024

Steel Column Erection



Multi-user Restroom Plumbing



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



W. H. MOSELEY MIDDLE SCHOOL (MS #6)

AS OF JANUARY 2024



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF JANUARY 2024

WORK COMPLETED AND ONGOING:

Site

- Northwest parking lot pouring complete; setting forms for southwest parking lot
- Moisture conditioning under southeast fire lanes ongoing
- North fire lane pours complete
- Storm drain lines around main building and MPF complete; working on laterals and storm drains along football field and practice field
- Water lines complete; working on offsite water line on Prairie Drive
- Sanitary sewer lines complete
- Parking lot light pole base drilling ongoing
- Gas line installation complete under north fire lane; continuing installation of gas line around MPF building
- Main electric easement laid out; waiting on CoServ to begin main electric underground

- Piers are complete on all ancillary buildings; grade beams ongoing – Area T
- Moisture conditioning at tennis courts ongoing
- First Street west bound turn lane ongoing; will transition to east bound turn lane

Building

- Main building piers complete
- Grade beams complete – Areas A, B, C, D, E, F, G, J, K, L, M, N, P, Q, R and S
- Slabs complete – Areas A, B and R; ongoing Area Q
- Fine grading for slab ongoing – Area C
- MEP underground complete – Areas A, B, Q, R and S; ongoing – Areas C and P
- Concrete columns ongoing – Area D and N
- Steel deliveries begin mid-January



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




RICHLAND HIGH SCHOOL (HS #4)

AS OF JANUARY 2024



LOOKING EAST
Richland High School

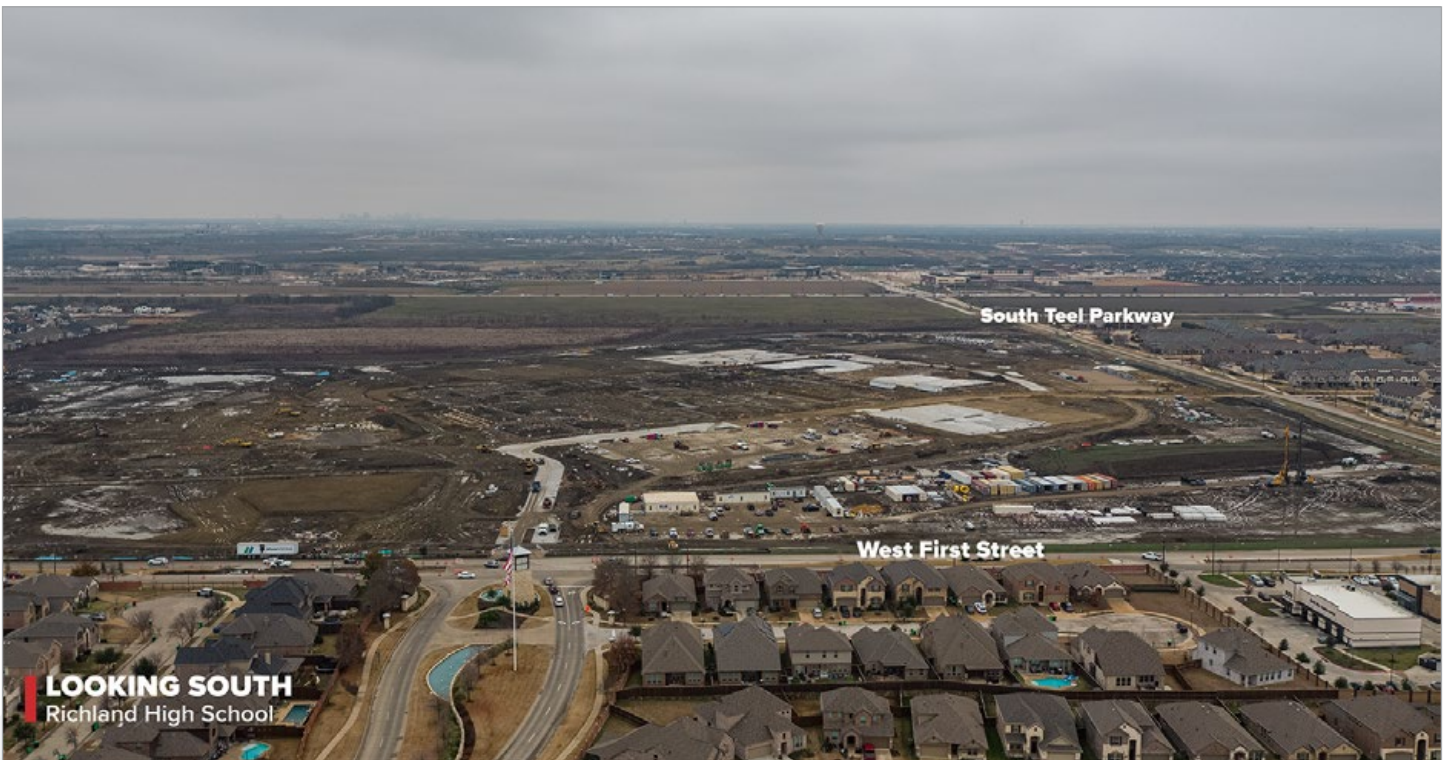

LOOKING SOUTH
Richland High School

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF JANUARY 2024



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF JANUARY 2024

Concrete Paving Formwork and Reinforcing



Completed Concrete Parking



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF JANUARY 2024

Auditorium Stage



Auditorium



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




RICHLAND HIGH SCHOOL (HS #4)

AS OF JANUARY 2024

Auditorium



Completed Concrete Foundation at West Academic Wing

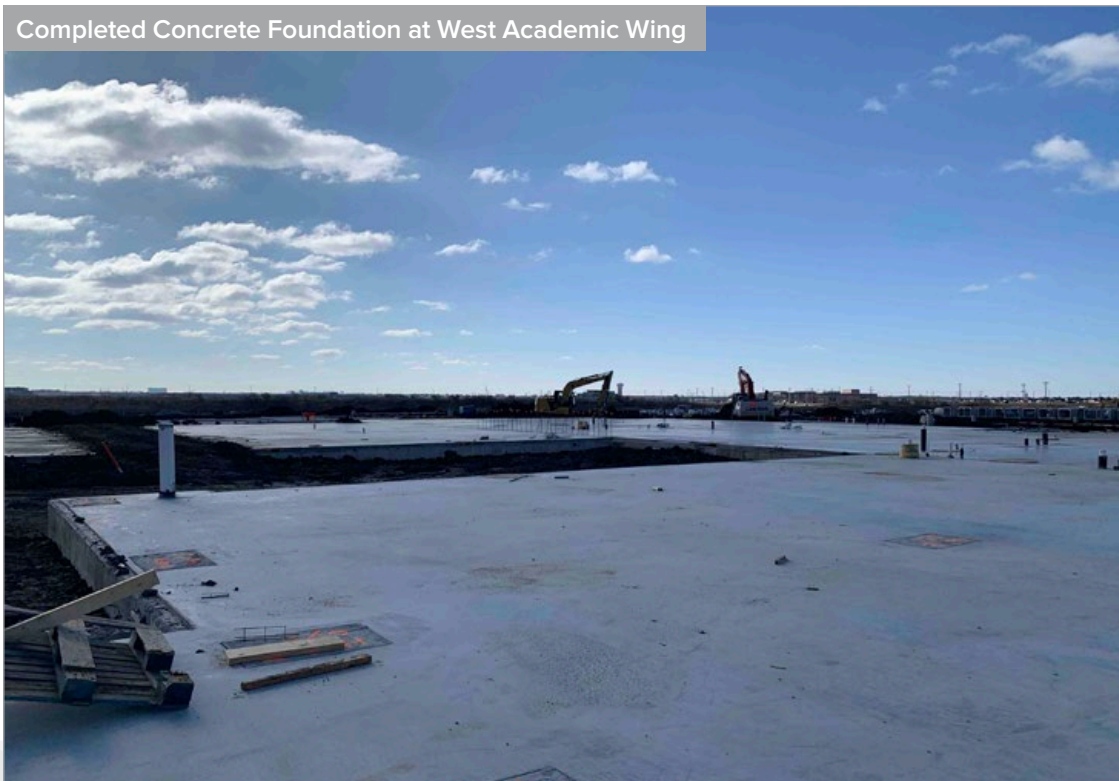

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



RICHLAND HIGH SCHOOL (HS #4)

AS OF JANUARY 2024

Completed Grade Beams and Pier Caps



Grade Beam Formwork and Reinforcing

